

Site Inspection Sheet

100223

Application

I H & J I FORRESTER
STONEWOOD HOMES
PO BOX 11036
SOCKBURN
CHRISTCHURCH 8443

Issue date

12/04/10

Project

Description	HOUSING - Detached Dwelling (New Dwellings Only) Being Stage 1 of an intended 1 Stages DOMESTIC DWELLING
Intended Life	Indefinite, but not less than 50 years
Intended Use	3 Bedroom Domestic Dwelling with Study & Attached Double Garage with Workshop - 300.14sqm2
Estimated Value	\$358,421
Location	28 SHERIDAN DRIVE, ROLLESTON
Legal Description	RAPID: LOT 148 DP 367715
Valuation No.	2405535748
Builder	



Code Compliance Certificate Sign-off Prompt Sheet

Ref: T-04 – PS-CCC

Version: 4

Iss: 24 Feb 2010

Page 1 of 2

A tick (✓) in any space indicates an item has been assessed / provided & is approved / acceptable

A cross (x) in any space indicates an item has not been assessed / provided and a comment / reason should be added

N / A should be used if an item is not applicable to the consent signoff process *5-11-10*

Owner: *I H + J I Forrester*

Consent N^o: *100 223*

Agent: *Storewood Homes.*

Complete all sections below using either ✓, x or N/A

✓ x
N/A

Comments / Reasons for decision

All listed inspections completed and copies of site inspection records in file:

✓

Have all consent conditions been met:

✓

Have energy works certificate(s) been supplied:

Electrical: *3283998 + 3365162*

Gas:

✓

Registration checked ok

N/A

List PS3(s) and PS4(s) supplied if any; in support of reasonable grounds:

1. *PS3 For Lina cladding installation*

✓

From Bevon McKeich Builders LTD

2.

3.

Compliance Schedule ok to issue; T&C notified & schedule / Statement produced. (One copy attached to CCC for sending to applicant; and one copy for file):

N/A

Has any other documentation been provided to support the issue of the CCC? List documents:

1. *Construction statement 1500 kPa Plumbing test.*

✓

Plumbers Registration checked.

2. *wet-seal Installation Certificate*

✓

3.

Is the owner(s) name correct:

(Check certificate of title if necessary)

✓

Has the mailing address been checked / updated:
(Use rates database or CCC application form)

✓

Check lawfully established use is correct, same as BC:
(E.g. detached dwelling, commercial etc). Ensure amendments have not altered description.

✓

Check legal description:

✓



Complete all sections below using either ✓, x or N/A	✓ x N/A	Comments / Reasons for decision
Check the location address aligns with Rates database:	✓	
Check year construction commenced (The year work started not the year consent was issued).	✓	2010 First Inspection
Confirm all NTF's (if any) have been complied with to allow the issuance of the CCC.	NA	
Further information requested:	NA	
All further information received and approved:	Signed: NA	Date:
CCC OK to Issue:	Signed: <i>GP Stevenson</i>	Date: 5-11-10
CCC Refused: (Provide reasoning).	Signed: NA	Date:
This signoff has been completed under the supervision of:	Signed:	Date:
This file /signoff has been reviewed by:	Signed:	Date:
		Date:

Date Reconciliation Completed:

Date Invoice Generated:

Date of Refund:

No further actions resulting from reconcile:



SCANNED

Form 6

**Code Compliance Certificate
Application**

(Only complete items that are applicable to your project)

FOR OFFICE USE ONLY

Building Consent No:

100223

Date Received:

16/9/10

100916029

APPLICATION

Street Address or Rapid No. as applicable: 28 Sheridan Drive	Legal Description: Lot: Valuation Roll Number:	DP:
Project Memorandum No.	Building Consent No. 100223	
Type of Building work: (eg. Domestic Dwelling)	Domestic Dwelling attached garage	
Building Consent issued by: (Name of Building Consent Authority)	Selwyn District Council	
Address Code Compliance Certificate to be posted to:	28 Sheridan Drive	

THE OWNER

Owner's Name: Iain Forrester	Contact Person: (if owner is a company) Paul Jenkins
Mailing/Billing Address: 28 Sheridan drive	
Street Address/Registered Office:	
E-mail Address:	
Phone Day:	Fax:
Cellphone: 0272 550012	

THE AGENT

Note - The Agent will be the first point of contact for communications with the Council/Building Consent Authority regarding this application/building work and will receive all correspondence including all invoices.

Agent's Name: Stonewood Homes		
Mailing/Billing Address: PO Box 11 036, Paparua		
Street Address/Registered Office:		
E-mail Address:		
Phone Day: 354 2344	Fax:	Cellphone: 0272 550012

KEY PERSONNEL

Designer:	Registration Number:
Mailing Address:	
E-mail Address:	Phone Day:
Engineer: Elliot Sinclair	Registration Number:
Mailing Address: 151 Kilmore St	
E-mail Address: rhw@elliott.co.nz	Phone Day: 3794014
Builder: Stonewood Homes	Registration Number:
Mailing Address: PO Box 11 036	
E-mail Address: paul@stonewood.co.nz	Phone Day: 0272 550012
Craftsman Plumber: Signature Plumbing	Registration Number:
Mailing Address: 16 Booker Ave	16161 ✓
E-mail Address: jallil@xtra.co.nz	Phone Day: 0274 574436

KEY PERSONNEL (continued)

Registered Drain layer: <i>Piperite Drainage</i>	Registration Number: <i>18538</i> ✓
Mailing Address: <i>83 Springs Rd, R01 Kapa</i>	
E-mail Address: <i>piperite@clearnet.nz</i>	Phone Day: <i>021 229 3015</i>
Registered Electrician: <i>KI Electrical</i>	Registration Number:
Mailing Address: <i>PO Box 26058</i>	
E-mail Address: <i>kjefectric@xtra.co.nz</i>	Phone Day: <i>02 74325327</i>
Craftsman Gasfitter: <i>N/A</i>	Registration Number:
Mailing Address:	<i>E3428</i> ✓
E-mail Address:	Phone Day:
Other:	Registration Number:
Mailing Address:	
E-mail Address:	Phone Day:

Add any additional relevant personnel on another sheet.

Other notes or comments which you as the applicant may wish to add

SIGNATURE

☒ Request for Issue of a Code Compliance Certificate for this work under Section 95 of the Building Act 2004.

Signed by or for and on behalf of the Owner:

☐ Owner

☒ Agent

Date:

16.9.10

Note: If acting "for and on behalf", please read & Initial the following declaration before signing: "I hereby declare that I am authorised to act as Agent of the Owner"

	Code Compliance Certificate Application Checklist - Form 6(C) (In conjunction with Form 6)	Building Consent No: <u>100 223</u>
		Date Received: <u>16/9/10</u>

Project address: 28 Sheridan Drive Rolleston

Have all the inspections listed in the Building Consent been carried out

YES / NO (Please circle) *Reinspection*

If NO, please book the inspection/s before proceeding with this application. *Reg*

NB The following is required on application in sufficient detail to show compliance with all aspects of the relevant Building Consent. Please complete this Checklist in FULL by placing a tick (✓) in the supplied or Not Applicable boxes. Additional information may be requested during processing of the application.

Check You Have Included -

COMPLETED, dated & signed Application Form

The Valuation number and Building Consent number

An Address for the CCC to be posted to

A copy of the Current Certificate of Title

Check You Have Listed The Key Personnel -

- Name, address, phone number, registration number for ALL key personnel

- e.g. Builder, Electrician, Drain layer, Plumber, etc

- Trade Certificates - provided for all key personnel

Check You Have Included The Documentation -

Electrical Certificate

Gas Certificate

Water Pressure Test (1500KPA) statement, if requested by Building Inspector

Producer Statement Construction (PS3) if required by Building Consent conditions

Producer Statement Construction Review (PS4) if required by Building Consent conditions

Proof of potability of water (3 tests results - 1 x chemical + 3 x bacteria)

Exterior Cladding - Construction Statement required by Building Consent conditions, e.g. Plaster Cladding, Classic Stone

Relocated Buildings - Copy of Code Compliance Certificate for the building, issued by the local authority whom's district the building was constructed in

Pile Driving records for driven piles

Septic tanks- Confirmation from ECAN that they have received and approved the certificate of construction from the drain layer / designer (Compliance Monitoring report)

Evidence that specified systems are capable of performing to the performance standards set out in the Building Consent including-

Installers Certificates

FPIS Certificates

Dangerous Goods Location - Test Certificate issued by an ERMA approved test certifier.

Approvals from Other Authorities - Approvals for discharges to land, air, or water from ECAN,

NOTE: Once received by the BCA, your CCC application will be considered and either issued or refused within 20 working days. Please note if any further information is requested this time is suspended until that information is received.

For BCA Use Only:-

This application is accepted / declined as all relevant information has / has not been supplied - signed:-

CONSTRUCTION STATEMENT- PIPEWORK TESTING

SELWYN DISTRICT COUNCIL

Building Consent Number:

SDC100223

Issued by:

(Registered Craftsman Plumber)

Joseph Horras

For:

(owner)

IAN + JEANETTE FORRESTER

In respect of the testing of water pipework prior to concealment

At:

(address)

28 SHERIDAN DRIVE

I hereby state that I have personally tested the water pipework installed in the building authorised under the above Building Consent by the method indicated hereunder:

- ☒ By pressurising the pipework to 1500 kpa for a period of not less than 15 minutes for the hot and cold water supply and checking to see that there are no leaks. (NZBC G12/AS1 7.5.1 (a),(b))
- ☒ By pressurising the upvc. pipework to 1.5 times the maximum working pressure for a period of not less than 15 minutes and checking that there are no leaks. (NZBC G12/AS1 7.5.2, NZS 7643)
- ☒ By pressurising the pipework to 1500 kpa for a period of not less than 5 minutes and checking to see that there are no leaks. (NZBC G12 VM1, AS3500:Part 1.2 1998)

For sanitary fixtures used for personal hygiene, I confirm that the tempering valve has been set so as to not exceed:

- ☐ 45°C for early childhood centres, schools, old people's homes, institutions for people with psychiatric or physical disabilities, hospitals. (G12/AS1 6.14.1(a))

or

- ☒ 55°C for all other buildings. (G12/AS1 6.14.1(b))

And I believe on reasonable grounds that the pipework has passed that test.

- ☒ All work complies with the NZBC

I also understand that the Christchurch City Council in accepting this construction statement will be relying on it to issue the code compliance certificate at the completion of the building work.

Signature of Craftsman Plumber:

[Signature]

Date:

23.7.10

Craftsman Registration No:

16161

Company Name:

Signature Plumbing LTD

PRODUCER STATEMENT CONSTRUCTION

ISSUED BY: Bevan McKeich Builders Ltd

TO: Selwyn District Council

IN RESPECT OF: External Cladding (Linea Weatherboard)


Bevan McKeich Builders Ltd has contracted to Stonewood Homes Ltd
(Contractor) (Employer/principal)

To carry out the above building works in accordance with the Contract titled

Lot 148 Sheridan Drive, Rolleston (new dwelling) consent 100223 ("the Contract")
(Project)

I, Bevan McKeich (*who holds Trade Certificate, Advanced Trade Certificate in carpentry, 25 years trade experience and a recognized James Hardie Installer*) a duly authorized representative of Bevan McKeich Builders Ltd believe on reasonable grounds that
(Contractor)

Bevan McKeich Builders Ltd have carried out and completed exterior cladding in accordance with the James Hardies Specifications, NZS 3604 and E2/AS1


.....
Bevan McKeich
(Signature of Authorized Agent on behalf of)

Date: 15 September 2010

Bevan McKeich Builders Ltd
(Contractor)

P O Box 69 199, Lincoln, 7640
(Address)



Wet-seal

Installation Certificate

Independent Franchisee of the Wet-seal Franchise System ("Wet-seal Franchisee"):

Gallagher Waterproofing Limited

PO Box 609, Rangiora, North Canterbury

Christchurch 7400

Invoice #: BE0877

Job Date: 25/08/10

Installation Address:

Stonewood Homes
PO BOX 11036
CHRISTCHURCH NZ Christ

Lot 273 Acacia Avenue
Rangiora NZ 8254

THIS CERTIFICATE given by the **Wet-seal** Franchisee certifies that: (a) the installations scheduled below ("**Work**") have been carried out at the above premises ("**Premises**") using the appropriate **Wet-seal** system of waterproofing; (b) the Work has been undertaken by the **Wet-seal** Franchisee; (c) the **Wet-seal** system of waterproofing used in the Work (i) complies with Australian/New Zealand Standard 4858; (ii) in respect of the Work carried out in Australia complies with the Building Code of Australia (BCA) as amended and complies with Australian Standard 3740; and (iii) in respect of the Work carried out in New Zealand complies with clause E2 (external moisture), clause E3 (internal moisture) of Compliance Document for New Zealand Building Code; (d) the **Wet-seal** system of waterproofing and the products used comprised in the Work have been (i) tested in respect of application and/or use in Australia by the Commonwealth Scientific and Industrial Research Organisations (CSIRO) as meeting the requirements of Australian Standard 4992; and (ii) appraised by BRANZ as appropriate for use in New Zealand.

For the Terms and Conditions, Special Conditions and Explanations please see the **Wet-seal** website www.wet-seal.ws. Any unauthorised alteration to this Certificate will invalidate it completely.

15 Years Workmanship Guarantee.*

Installations ("**Work**"):

Area:	Location:	Shower Type:	Bath Type:	Notes:
BATHROOM Under Tile Heating	Ground Floor			Undertile heating to bathroom & ensuite

I understand this Producer Statement will be relied on by Council to confirm compliance with the Building Code and/or conditions of the Building Consent to which it relates.

Steven Gallagher - authorised signatory for and on behalf of Wet-seal Franchisee

* The guarantee of workmanship in relation to this Installation Certificate lasts 15 years to comply with local authority requirements and the Weathertight Homes Resolution Services Act 2006. However, pursuant to Section 393 of the Building Act 2004 civil proceedings relating to building work may not be brought against Wet-seal after 10 years or more from the date of the act or omission on which the proceedings are based so please note this.

Warranty - The **Wet-seal** Franchisee warrants that the Work has been completed in a proper and workmanlike manner. The franchisor ("**Franchisor**") of the **Wet-seal** system is not liable in any respect under this warranty and the **Wet-seal** Franchisee's liability is limited to the costs only of removing and replacing affected installations. In the event of any warranty claim being made the **Wet-seal** Franchisee has the right prior to being obliged to carry out any remedial work, to enter the Premises (together with inspectors and/or advisers including but not limited to the Franchisor) and to inspect the Work and to carry out such remedial work as it deems fit. This warranty does not cover damage to the Work caused by any third party.

Certified System
Quality
ISO 9001

BRANZ Appraised
Approved / No. 486 (2005)
Ref: WS(C0909)



Wet-seal

Installation Certificate

Independent Franchisee of the Wet-seal Franchise System ("Wet-seal Franchisee"):

Gallagher Waterproofing Limited
PO Box 609, Rangiora, North Canterbury
Christchurch 7400

Invoice #: BE0880
Job Date: 25/08/10

Stonewood Homes
PO BOX 11036
CHRISTCHURCH NZ Christ

Installation Address:

Lot 148 #28 Sheridan Drive
Rolleston NZ 8004

THIS CERTIFICATE given by the **Wet-seal** Franchisee certifies that: (a) the installations scheduled below ("**Work**") have been carried out at the above premises ("**Premises**") using the appropriate **Wet-seal** system of waterproofing; (b) the **Work** has been undertaken by the **Wet-seal** Franchisee; (c) the **Wet-seal** system of waterproofing used in the **Work** (i) complies with Australian/New Zealand Standard 4858; (ii) in respect of the **Work** carried out in Australia complies with the Building Code of Australia (BCA) as amended and complies with Australian Standard 3740; and (iii) in respect of the **Work** carried out in New Zealand complies with clause E2 (external moisture), clause E3 (internal moisture) of Compliance Document for New Zealand Building Code; (d) the **Wet-seal** system of waterproofing and the products used comprised in the **Work** have been (i) tested in respect of application and/or use in Australia by the Commonwealth Scientific and Industrial Research Organisations (CSIRO) as meeting the requirements of Australian Standard 4992; and (ii) appraised by BRANZ as appropriate for use in New Zealand.

For the Terms and Conditions, Special Conditions and Explanations please see the **Wet-seal** website www.wet-seal.ws. Any unauthorised alteration to this Certificate will invalidate it completely.

15 Years Workmanship Guarantee.*

Installations ("**Work**"):

Area:	Location:	Shower Type:	Bath Type:	Notes:
BATHROOM	Ground Floor	STEP DOWN Shower Wall Tanked		
ENSUITE	Ground Floor	STEP DOWN Shower Wall Tanked	ISLAND Bath OverFlashed Bath Not Fitted	

I understand this Producer Statement will be relied on by Council to confirm compliance with the Building Code and/or conditions of the Building Consent to which it relates.

Steven Gallagher - authorised signatory for and on behalf of Wet-seal Franchisee

* The guarantee of workmanship in relation to this Installation Certificate lasts 15 years to comply with local authority requirements and the Weathertight Homes Resolution Services Act 2006. However, pursuant to Section 393 of the Building Act 2004 civil proceedings relating to building work may not be brought against Wet-seal after 10 years or more from the date of the act or omission on which the proceedings are based so please note this.



Warranty - The **Wet-seal** Franchisee warrants that the **Work** has been completed in a proper and workmanlike manner. The franchisor ("**Franchisor**") of the **Wet-seal** system is not liable in any respect under this warranty and the **Wet-seal** Franchisee's liability is limited to the costs only of removing and replacing affected installations. In the event of any warranty claim being made the **Wet-seal** Franchisee has the right prior to being obliged to carry out any remedial work, to enter the Premises (together with inspectors and/or advisers including but not limited to the Franchisor) and to inspect the **Work** and to carry out such remedial work as it deems fit. This warranty does not cover damage to the **Work** caused by any third party.

BRANZ Appraised
Approval No A96 [2005]
Ref: WSC099

100 917051

Form 6


FOR OFFICE USE ONLY

Building Consent No:

Date Received:

17 SEP 2010

SCANNED

Code Compliance Certificate
Application

(Only complete items that are applicable to your project)

APPLICATION

Street Address or Rapid No. as applicable:

28 Sheridan Drive

Legal Description: Lot: 148 DP: 367715

Valuation Roll Number: 2405535748

Project Memorandum No.

Building Consent No. 100223

Type of Building Work: (eg. Domestic Dwelling)

Domestic Dwelling attached garage

Building Consent issued by:

(Name of Building Consent Authority)

Selwyn District Council

Address Code Compliance Certificate to be posted to:

28 Sheridan Drive

THE OWNER

Owner's Name:

Ian Forrester

Contact Person:

(If owner is a company)

Paul Jenkins

Mailing/Billing Address:

28 Sheridan Drive

Street Address/Registered Office:

E-mail Address:

Phone Day:

Fax:

Cellphone: 0272 550012

THE AGENT

Note - The Agent will be the first point of contact for communications with the Council/Building Consent Authority regarding this application/building work and will receive all correspondence including all invoices.

Agent's Name:

Stonewood Homes

Mailing/Billing Address:

PO Box 11 036, Papanui

Street Address/Registered Office:

E-mail Address:

Phone Day:

354 2344

Fax:

Cellphone: 0272 550012

KEY PERSONNEL

Designer:

Registration Number:

Mailing Address:

E-mail Address:

Phone Day:

Engineer:

Elliot Sinclair

Registration Number:

Mailing Address:

151 Kilmore St

E-mail Address:

rh@elliott.co.nz

Phone Day: 3794014

Builder:

Stonewood Homes

Registration Number:

Mailing Address:

PO Box 11 036

E-mail Address:

paul@stonewood.co.nz

Phone Day: 0272 550012

Craftsman Plumber:

Signature Plumbing

Registration Number:

Mailing Address:

16 Booker Ave

16161

E-mail Address:

jnl11@xtra.co.nz

Phone Day: 0274 514436



KEY PERSONNEL (continued)

Registered Drain layer: <i>Piperite Drainage</i>		Registration Number:
Mailing Address: <i>83 Youngs Rd, RDI Kuopu</i>		<i>18538</i>
E-mail Address: <i>piperite@clear.net.nz</i>	Phone Day: <i>0212293015</i>	
Registered Electrician: <i>KI Electrical</i>		Registration Number:
Mailing Address: <i>PO Box 26058</i>		<i>3428</i>
E-mail Address: <i>kjet@electricity.co.nz</i>	Phone Day: <i>02 74325327</i>	
Craftsman Gasfitter: <i>N/A</i>		Registration Number:
Mailing Address:		<i>3428</i>
E-mail Address:	Phone Day:	
Other:		Registration Number:
Mailing Address:		
E-mail Address:	Phone Day:	

Add any additional relevant personnel on another sheet.

Other notes or comments which you as the applicant may wish to add

SIGNATURE

☒ Request for issue of a Code Compliance Certificate for this work under Section 95 of the Building Act 2004.

Signed by or for and on behalf of the Owner:

☐ Owner ☒ Agent

Date:

16-9-10

Note: If acting "for and on behalf", please read & initial the following declaration before signing: "I hereby declare that I am authorised to act as Agent of the Owner".....





Selwyn
DISTRICT COUNCIL

**Code Compliance Certificate
Application Checklist - Form 6(C)**
(in conjunction with Form 6)

Building Consent No:

100223

Date Received:

Project address:

Have all the inspections listed in the Building Consent been carried out

YES / NO (Please circle)

If NO, please book the inspection/s before proceeding with this application.

NB The following is required on application in sufficient detail to show compliance with all aspects of the relevant Building Consent. Please complete this Checklist in FULL by placing a tick (✓) in the supplied or Not Applicable boxes. Additional Information may be requested during processing of the application.

Supplied

Not Applicable

Selwyn BCA Use Only

Check You Have Included -

COMPLETED, dated & signed Application Form

The Valuation number and Building Consent number

An Address for the CCC to be posted to

A copy of the Current Certificate of Title

Check You Have Listed The Key Personnel -

- Name, address, phone number, registration number for ALL key personnel

- e.g. Builder, Electrician, Drain layer, Plumber, etc

- Trade Certificates - provided for all key personnel

Check You Have Included The Documentation -

Electrical Certificate

Gas Certificate

Water Pressure Test (1500KPA) statement, if requested by Building Inspector

Producer Statement Construction (PS3) if required by Building Consent conditions

Producer Statement Construction Review (PS4) if required by Building Consent conditions

Proof of potability of water (3 tests results - 1 x chemical + 3 x bacteria)

Exterior Cladding - Construction Statement required by Building Consent conditions, e.g.

Plaster Cladding, Classic Stone

Relocated Buildings - Copy of Code Compliance Certificate for the building, issued by the local authority whom's district the building was constructed in

Pile Driving records for driven piles

Septic tanks- Confirmation from ECAN that they have received and approved the certificate of construction from the drain layer / designer (Compliance Monitoring report)

Evidence that specified systems are capable of performing to the performance standards set out in the Building Consent including-

Installers Certificates

FPIS Certificates

Dangerous Goods Location - Test Certificate issued by an ERMA approved test certifier.

Approvals from Other Authorities - Approvals for discharges to land, air, or water from ECAN,

NOTE: Once received by the BCA, your CCC application will be considered and either issued or refused within 20 working days. Please note if any further information is requested this time is suspended until that information is received.

For BCA Use Only:-

This application is accepted / declined as all relevant information has / has not been supplied - signed:-



Further Information Requested:

Additional BC & CCC Work

Date	Initials	Administration	Units

Date	Initials	Processing	Units
30-7-10		Research (John Haddon)	SEE times research
5-11-10	CDS	CCC	5

Date	Initials	Extra & Re-inspections	Units	Travel	Mileage
		2 extra prelims - Daryl & Carl			
3-08-10	CDS	Reinspect Prelims	3	1	2
22-09-10	CDS	Reinspection final	5	1	4

Code Compliance Certificate**100223****Section 95, Building Act 2004**

COPY

The Owner

Name of Owner: Forrester Ian Howard & Forrester Jeanette Irene
Mailing address: 28 Sheridan Drive, Rolleston 7614
Street address/registered office:
Phone number:
Landline: Daytime: 347 9322
Mobile: After hours:
Facsimile number:
Email address:
Website:

The Building Work

Street Address of Building: 28 SHERIDAN DRIVE, ROLLESTON
Legal Description of land where building is located: LOT 148 DP 367715
Valuation Number: 2405535748
Current lawfully established use: DETACHED DWELLING
Type of work: 3 BEDROOM DOMESTIC DWELLING WITH STUDY AND ATTACHED DOUBLE GARAGE
Estimated Value: \$358,421
Location of building within site/block number:
Building Name: Year Construction Commenced: 2010

Code Compliance Certificate:

The Building Consent Authority named above is satisfied on reasonable grounds, that the Building work complies with the Building Consent



Selwyn District Council Building Consent Authority Signatory

Issue Date: 5/11/10



INSPECTION NOTICE

Inspections are to be booked by the owner or builder

Name: **STONEWOOD HOMES**

Consent No: **100223**

Site Address/Rapid No

Officer ID: AOFSTEVEG

28 SHERIDAN DRIVE, ROLLESTON

Name: Geoff Stevenson

Type of building work:

Intended Use: : 3 Bedroom Domestic Dwelling with Study & Attached Double Garage with Workshop - 300.14sqm2
DOMESTIC DWELLING

Stats Code: HOUSING - Detached Dwelling (New Dwellings Only)

On 3/11/2010 at 8:29 a.m. this site was inspected pursuant to the Building Act 2004 (section 222/230) and the Local Government Act 2004 (Section 174). The purpose of the inspection was:

INSPECTION TYPE: PRACT COMPLETION (HABITABLE)

INSPECTION RESULT: BUILDING WORK MAY PROCEED

The Following Items are yet to be completed:

Notes Summary:

Item on notice dated 22/09/10 appears to be completed. Flashing in place. unable to see if flashing is sealed to wrap. Accepted to be completed as per requirements on reasonable grounds.

CCC application with supporting documents with inspection notes.

Note: A Code Compliance Certificate is required for 2004 Building Act Consents

INSTRUCTIONS

Notice To:	Contractor ☐	Owner ☐	Agent ☐	Occupier	ENTERED
By:	Telephone ☐	Fax ☐	Posting ☐	Left on Site	



INSPECTION NOTICE

Inspections are to be booked by the owner or builder

Name: **STONEWOOD HOMES**

Consent No: **100223**

Site Address/Rapid No

Officer ID: AOFSTEVEG

28 SHERIDAN DRIVE, ROLLESTON

Name: Geoff Stevenson

Type of building work:

Intended Use: : 3 Bedroom Domestic Dwelling with Study & Attached Double Garage with Workshop - 300.14sqm2
DOMESTIC DWELLING

Stats Code: HOUSING - Detached Dwelling (New Dwellings Only)

On 3/11/2010 at 8:29 a.m. this site was inspected pursuant to the Building Act 2004 (section 222/230) and the Local Government Act 2004 (Section 174). The purpose of the inspection was:

INSPECTION TYPE: PRACT COMPLETION (HABITABLE)

INSPECTION RESULT: BUILDING WORK MAY PROCEED

The Following Items are yet to be completed:

Notes Summary:

Item on notice dated 22/09/10 appears to be completed. Flashing in place. unable to see if flashing is sealed to wrap. Accepted to be completed as per requirements on reasonable grounds.

CCC application with supporting documents with inspection notes.

Note: A Code Compliance Certificate is required for 2004 Building Act Consents

INSTRUCTIONS

Notice To:	Contractor ☐	Owner ☐	Agent ☐	Occupier	
By:	Telephone ☐	Fax ☐	Posting ☐	Left on Site	

Consent No: 100 223

Applicants Name: _____

Date: 8 110 110**MEMO**

Driveby to inspect Linen to brick sill
after receiving advice from Paul Jenkins
Storewood Homes that all work had been
completed. Flashing has not been installed
Requested that a reinspection be booked
with SDC when completed, to meet
the performance requirements of NZBC

Signed AM Stevenson



The home you deserve

Stonewood Homes
PO Box 11 036
Papanui
Christchurch

October 7, 2010

Re: SDC100223

To the inspections team:

I can confirm that ALL items on the final inspection sheet dated 16/9/10 in relation to the code of compliance inspection at 28 Sheridan Drive have been completed.

Items 1,2,3,5 and 6 have been signed off by your inspector at time of re inspection. Item 6 was however incomplete at this time. Following a site visit this afternoon I can confirm that the linea under the bedroom window has sufficient clearance to the brick sill.

Please advise if you wish to conduct a re inspection or if this Producer Statement is sufficient enough for you to issue the code of compliance.

Yours truly,

Paul Jenkins
Building Manager
Stonewood Homes
027 255 0012
Paul@stonewood.co.nz



7 OCT 2010

Phone: +64 3 354 2344

Fax: +64 3 354 2342

204 Main North Road, PO Box 11036

Christchurch 8051, New Zealand

info@stonewood.co.nz



0800 860 000 | www.stonewood.co.nz



INSPECTION NOTICE

Inspections are to be booked by the owner or builder

Name: **STONEWOOD HOMES**

Consent No: **100223**

Site Address/Rapid No

Officer ID: **AOFSTEVEG**

28 SHERIDAN DRIVE, ROLLESTON

Name: **Geoff Stevenson**

Type of building work:

Intended Use: : 3 Bedroom Domestic Dwelling with Study & Attached Double Garage with Workshop - 300.14sqm2
DOMESTIC DWELLING

Stats Code: **HOUSING - Detached Dwelling (New Dwellings Only)**

On 16/09/2010 at 2:16 p.m. this site was inspected pursuant to the Building Act 2004 (section 222/230) and the Local Government Act 2004 (Section 174). The purpose of the inspection was:

INSPECTION TYPE: PRACT COMPLETION (HABITABLE)

INSPECTION RESULT: BUILDING WORK MAY NOT PROCEED/REINSPECTION REQUIRED

The Following Items are yet to be completed:

1 Down lights Clear of insulation if not CA rated (Interior)

1/ At least one down light still to be cut clear of insulation & insulation reinstalled over kitchen area. Please check all down lights.

Sealing of Bathroom Fixtures (Interior)

2/ Seal top of tiled shower trim to walls. Both showers.

Safety Glass (Interior)

3/ Install permanent shower screens.

Other

4/ Provide clearance to bottom of linea panel to linea specification, master bedroom window.

5/ Fix all exterior heat pump units to concrete.

6/ Complete the sealing of driveway + associated drainage

Notes Summary:


Ceiling space insulation tidy. Down lights have insulation abutting. Ensure to manufactures specification. Plumbing frost protection completed. Smoke alarms installed. Sealing of wet areas completed. Safety glass installed windows. HWC seismic restraints, valving, Copper drain completed. Waste connection + venting completed. Sealing of wet areas completed. Drain venting in place. Landscaping still to complete, ensure ground levels are maintained in accordance with NZBC E2 AS1.

DOCUMENTS accepted by inspector. CCC on hold untill final has passed. 1/ Electrical energy certificate. 2/ Plumbing 1500 KPA test certificate.3/ Completed Code Compliance Application.

Note: A Code Compliance Certificate is required for 2004 Building Act Consents

INSTRUCTIONS

Notice To:	Contractor ☐	Owner ☐	Agent ☐	Occupier	
By:	Telephone ☐	Fax ☐	Posting ☐	Left on Site	



Form 6

Code Compliance Certificate
Application

(Only complete items that are applicable to your project)

FOR OFFICE USE ONLY

Building Consent No:

Date Received:

APPLICATION

Street Address or Rapid No. as applicable: <i>28 Sheridan Drive</i>	Legal Description: Lot: DP:
	Valuation Roll Number:
Project Memorandum No.:	Building Consent No. <i>100223</i>
Type of Building work: (eg. Domestic Dwelling)	<i>Domestic Dwelling attached garage</i>
Building Consent Issued by: (Name of Building Consent Authority)	<i>Selwyn District Council</i>
Address Code Compliance Certificate to be posted to: <i>28 Sheridan Drive</i>	

THE OWNER

Owner's Name: <i>Iain Forrester</i>	Contact Person: (if owner is a company) <i>Paul Jenkins</i>
Mailing/Billing Address: <i>28 Sheridan Drive</i>	
Street Address/Registered Office:	
E-mail Address:	
Phone Day:	Fax:
	Cellphone: <i>0272 550012</i>

THE AGENT

Note - The Agent will be the first point of contact for communications with the Council/Building Consent Authority regarding this application/building work and will receive all correspondence including all invoices.

Agent's Name: <i>Stonewood Homes</i>	
Mailing/Billing Address: <i>PO Box 11 036, Paparua</i>	
Street Address/Registered Office:	
E-mail Address:	
Phone Day: <i>354 2344</i>	Cellphone: <i>0272 550012</i>

KEY PERSONNEL

Designer:	Registration Number:
Mailing Address:	
E-mail Address:	Phone Day:
Engineer: <i>Elliot Sinclair</i>	Registration Number:
Mailing Address: <i>151 Kilmore St</i>	
E-mail Address: <i>rhwa@elliott.co.nz</i>	Phone Day: <i>3794014</i>
Builder: <i>Stonewood Homes</i>	Registration Number:
Mailing Address: <i>PO Box 11 036</i>	
E-mail Address: <i>paul@stonewood.co.nz</i>	Phone Day: <i>0272 550012</i>
Craftsman Plumber: <i>Signature Plumbing</i>	Registration Number:
Mailing Address: <i>16 Booker Ave</i>	<i>16161</i>
E-mail Address: <i>jan111@xtra.co.nz</i>	Phone Day: <i>0274 574436</i>



	Code Compliance Certificate Application Checklist - Form 6(C) (In conjunction with Form 6)	Building Consent No:
		Date Received:

Project address:

Have all the inspections listed in the Building Consent been carried out

YES / NO (Please circle)

If NO, please book the inspection/s before proceeding with this application.

NB The following is required on application in sufficient detail to show compliance with all aspects of the relevant Building Consent. Please complete this Checklist in FULL by placing a tick (✓) in the supplied or Not Applicable boxes. Additional information may be requested during processing of the application.

Check You Have Included -

COMPLETED, dated & signed Application Form

The Valuation number and Building Consent number

An Address for the CCC to be posted to

A copy of the Current Certificate of Title

Check You Have Listed The Key Personnel -

- Name, address, phone number, registration number for ALL key personnel

- e.g. Builder, Electrician, Drain layer, Plumber, etc

- Trade Certificates - provided for all key personnel

Check You Have Included The Documentation -

Electrical Certificate

Gas Certificate

Water Pressure Test (1500KPA) statement, if requested by Building Inspector

Producer Statement Construction (PS3) if required by Building Consent conditions

Producer Statement Construction Review (PS4) if required by Building Consent conditions

Proof of potability of water (3 tests results - 1 x chemical + 3 x bacteria)

Exterior Cladding - Construction Statement required by Building Consent conditions, e.g.

Plaster Cladding, Classic Stone

Relocated Buildings - Copy of Code Compliance Certificate for the building, issued by the local authority whom's district the building was constructed in

Pile Driving records for driven piles

Septic tanks- Confirmation from ECAN that they have received and approved the certificate of construction from the drain layer / designer (Compliance Monitoring report)

Evidence that specified systems are capable of performing to the performance standards set out in the Building Consent including-

Installers Certificates

FPIS Certificates

Dangerous Goods Location - Test Certificate issued by an ERMA approved test certifier.

Approvals from Other Authorities - Approvals for discharges to land, air, or water from ECAN,

NOTE: Once received by the BCA, your CCC application will be considered and either issued or refused within 20 working days. Please note if any further information is requested this time is suspended until that information is received.

For BCA Use Only:-

This application is accepted / declined as all relevant information has / has not been supplied - signed:-

KEY PERSONNEL (continued)

Registered Drain layer: <u>Piperide Drainage</u>	Registration Number: <u>18538</u>
Mailing Address: <u>83 Springs Rd, RD1 Kuopu</u>	
E-mail Address: <u>piperide@clear.net.nz</u>	Phone Day: <u>021 2293015</u>
Registered Electrician: <u>KI Electrical</u>	Registration Number:
Mailing Address: <u>PO Box 26058</u>	
E-mail Address: <u>kjelectrical@xtra.co.nz</u>	Phone Day: <u>02 74325327</u>
Craftsman Gasfitter: <u>N/A</u>	Registration Number:
Mailing Address:	<u>3428</u>
E-mail Address:	Phone Day:
Other:	Registration Number:
Mailing Address:	
E-mail Address:	Phone Day:

Add any additional relevant personnel on another sheet.

Other notes or comments which you as the applicant may wish to add

SIGNATURE

☒ Request for Issue of a Code Compliance Certificate for this work under Section 95 of the Building Act 2004.

Signed by or for and on behalf of the Owner:

☐

Owner

☒

Agent

Date:

16-9-10

Note: If acting "for and on behalf", please read & Initial the following declaration before signing: "I hereby declare that I am authorised to act as Agent of the Owner".....

CONSTRUCTION STATEMENT- PIPEWORK TESTING

SELWYN DISTRICT COUNCIL

Building Consent Number:

SDC100223

Issued by:

(Registered Craftsman Plumber)

Joseph Heras

For:

(owner)

IAN + SEANETTE FORRESTER

In respect of the testing of water pipework prior to concealment

At:

(address)

28 SHERIDAN DRIVE

I hereby state that I have personally tested the water pipework installed in the building authorised under the above Building Consent by the method indicated hereunder:

- ☒ By pressurising the pipework to 1500 kpa for a period of not less than 15 minutes for the hot and cold water supply and checking to see that there are no leaks. (NZBC G12/AS1 7.5.1 (a),(b))
- ☒ By pressurising the upvc. pipework to 1.6 times the maximum working pressure for a period of not less than 15 minutes and checking that there are no leaks. (NZBC G12/AS1 7.5.2, NZS 7643)
- ☒ By pressurising the pipework to 1500 kpa for a period of not less than 5 minutes and checking to see that there are no leaks. (NZBC G12 VM1, AS3500:Part 1.2 1998)

For sanitary fixtures used for personal hygiene, I confirm that the tempering valve has been set so as to not exceed:

☐ 45°C for early childhood centres, schools, old people's homes, institutions for people with psychiatric or physical disabilities, hospitals. (G12/AS1 6.14.1(a))

or

☒ 55°C for all other buildings. (G12/AS1 6.14.1(b))

And I believe on reasonable grounds that the pipework has passed that test.

☒ All work complies with the NZBC

I also understand that the Christchurch City Council in accepting this construction statement will be relying on it to issue the code compliance certificate at the completion of the building work.

Signature of Craftsman Plumber:

Date:

Craftsman Registration No:

Company Name:


23.7.10
16161
Signature Plumbing LTD

PRODUCER STATEMENT CONSTRUCTION

ISSUED BY: Bevan McKeich Builders Ltd

TO: Selwyn District Council

IN RESPECT OF: External Cladding (Linea Weatherboard)


Bevan McKeich Builders Ltd has contracted to Stonewood Homes Ltd
(Contractor) (Employer/principal)

To carry out the above building works in accordance with the Contract titled

Lot 148 Sheridan Drive, Rolleston (new dwelling) consent 100223 ("the Contract")
(Project)

I, Bevan McKeich (*who holds Trade Certificate, Advanced Trade Certificate in carpentry, 25 years trade experience and a recognized James Hardie Installer*) a duly authorized representative of Bevan McKeich Builders Ltd believe on reasonable grounds that
(Contractor)

Bevan McKeich Builders Ltd have carried out and completed exterior cladding in accordance with the James Hardies Specifications, NZS 3604 and E2/AS1


.....
Bevan McKeich
(Signature of Authorized Agent on behalf of)

Date: 15 September 2010

Bevan McKeich Builders Ltd
(Contractor)

P O Box 69 199, Lincoln, 7640
(Address)



Wet-seal

Installation Certificate

Independent Franchisee of the Wet-seal Franchise System ("Wet-seal Franchisee"):

Gallagher Waterproofing Limited
PO Box 609, Rangiora, North Canterbury
Christchurch 7400

Invoice #: BE0877
Job Date: 25/08/10

Stonewood Homes
PO BOX 11036
CHRISTCHURCH NZ Christ

Installation Address:

Lot 273 Acacia Avenue
Rangiora NZ 8254

THIS CERTIFICATE given by the Wet-seal Franchisee certifies that: (a) the installations scheduled below ("Work") have been carried out at the above premises ("Premises") using the appropriate Wet-seal system of waterproofing; (b) the Work has been undertaken by the Wet-seal Franchisee; (c) the Wet-seal system of waterproofing used in the Work (i) complies with Australian/New Zealand Standard 4858; (ii) in respect of the Work carried out in Australia complies with the Building Code of Australia (BCA) as amended and complies with Australian Standard 3740; and (iii) in respect of the Work carried out in New Zealand complies with clause E2 (external moisture), clause E3 (internal moisture) of Compliance Document for New Zealand Building Code; (d) the Wet-seal system of waterproofing and the products used comprised in the Work have been (i) tested in respect of application and/or use in Australia by the Commonwealth Scientific and Industrial Research Organisations (CSIRO) as meeting the requirements of Australian Standard 4992; and (ii) appraised by BRANZ as appropriate for use in New Zealand.

For the Terms and Conditions, Special Conditions and Explanations please see the Wet-seal website www.wet-seal.ws. Any unauthorised alteration to this Certificate will invalidate it completely.

15 Years Workmanship Guarantee.*

Installations ("Work"):

Area:	Location:	Shower Type:	Bath Type:	Notes:
BATHROOM Under Tile Heating	Ground Floor			Undertile heating to bathroom & ensuite

I understand this Producer Statement will be relied on by Council to confirm compliance with the Building Code and/or conditions of the Building Consent to which it relates.

Steven Gallagher - authorised signatory for and on behalf of Wet-seal Franchisee

* The guarantee of workmanship in relation to this Installation Certificate lasts 15 years to comply with local authority requirements and the Weathertight Homes Resolution Services Act 2006. However, pursuant to Section 393 of the Building Act 2004 civil proceedings relating to building work may not be brought against Wet-seal after 10 years or more from the date of the act or omission on which the proceedings are based so please note this.

Certified System
Quality
ISO 9001

Warranty - The Wet-seal Franchisee warrants that the Work has been completed in a proper and workmanlike manner. The franchisor ("Franchisor") of the Wet-seal system is not liable in any respect under this warranty and the Wet-seal Franchisee's liability is limited to the costs only of removing and replacing affected installations. In the event of any warranty claim being made the Wet-seal Franchisee has the right prior to being obliged to carry out any remedial work, to enter the Premises (together with inspectors and/or advisers including but not limited to the Franchisor) and to inspect the Work and to carry out such remedial work as it deems fit. This warranty does not cover damage to the Work caused by any third party.

BRANZ Appraised
Appraisal No. 486 [2009]
Ref: WS/06909

•
•

•
•



Wet-seal

Installation Certificate

Independent Franchisee of the Wet-seal Franchise System ("Wet-seal Franchisee"):

Gallagher Waterproofing Limited

PO Box 609, Rangiora, North Canterbury

Christchurch 7400

Invoice #: BE0880

Job Date: 25/08/10

Stonewood Homes
PO BOX 11036
CHRISTCHURCH NZ Christ

Installation Address:

Lot 148 #28 Sheridan Drive
Rolleston NZ 8004

THIS CERTIFICATE given by the **Wet-seal** Franchisee certifies that: (a) the installations scheduled below ("**Work**") have been carried out at the above premises ("**Premises**") using the appropriate **Wet-seal** system of waterproofing; (b) the Work has been undertaken by the **Wet-seal** Franchisee; (c) the **Wet-seal** system of waterproofing used in the Work (i) complies with Australian/New Zealand Standard 4858; (ii) in respect of the Work carried out in Australia complies with the Building Code of Australia (BCA) as amended and complies with Australian Standard 3740; and (iii) in respect of the Work carried out in New Zealand complies with clause E2 (external moisture), clause E3 (internal moisture) of Compliance Document for New Zealand Building Code; (d) the **Wet-seal** system of waterproofing and the products used comprised in the Work have been (i) tested in respect of application and/or use in Australia by the Commonwealth Scientific and Industrial Research Organisations (CSIRO) as meeting the requirements of Australian Standard 4992; and (ii) appraised by BRANZ as appropriate for use in New Zealand.

For the Terms and Conditions, Special Conditions and Explanations please see the **Wet-seal** website www.wet-seal.ws. Any unauthorised alteration to this Certificate will invalidate it completely.

15 Years Workmanship Guarantee.*

Installations ("**Work**"):

Area:	Location:	Shower Type:	Bath Type:	Notes:
BATHROOM	Ground Floor	STEP DOWN Shower Wall Tanked		
ENSUITE	Ground Floor	STEP DOWN Shower Wall Tanked	ISLAND Bath OverFlashed Bath Not Fitted	

I understand this Producer Statement will be relied on by Council to confirm compliance with the Building Code and/or conditions of the Building Consent to which it relates.

Steven Gallagher - authorised signatory for and on behalf of Wet-seal Franchisee

* The guarantee of workmanship in relation to this Installation Certificate lasts 15 years to comply with local authority requirements and the Weathertight Homes Resolution Services Act 2006. However, pursuant to Section 393 of the Building Act 2004 civil proceedings relating to building work may not be brought against Wet-seal after 10 years or more from the date of the act or omission on which the proceedings are based so please note this.

Certified System
Quality
ISO 9001

Warranty - The **Wet-seal** Franchisee warrants that the Work has been completed in a proper and workmanlike manner. The franchisor ("**Franchisor**") of the **Wet-seal** system is not liable in any respect under this warranty and the **Wet-seal** Franchisee's liability is limited to the costs only of removing and replacing affected installations. In the event of any warranty claim being made the **Wet-seal** Franchisee has the right prior to being obliged to carry out any remedial work, to enter the Premises (together with inspectors and/or advisers including but not limited to the Franchisor) and to inspect the Work and to carry out such remedial work as it deems fit. This warranty does not cover damage to the Work caused by any third party.

BRANZ Appraised
Approval No. 4086 (2005)
Ref: WSG0999

1. The first part of the document discusses the importance of maintaining accurate records of all transactions.

2. It is essential to ensure that all data is entered correctly and consistently.

3. The second part of the document outlines the procedures for handling discrepancies.

4. It is important to identify the source of the error and take appropriate corrective action.

5. The third part of the document provides a detailed explanation of the audit process.

6. This section includes a list of the documents and records that will be reviewed.

7. The fourth part of the document discusses the results of the audit.

8. The findings of the audit are summarized in the following table:

9. The table shows the number of errors identified in each category.

10. The fifth part of the document provides recommendations for improving the system.

11. These recommendations are based on the findings of the audit and are intended to prevent future errors.

12. The sixth part of the document discusses the implementation of the recommendations.

13. It is important to ensure that all staff are trained on the new procedures.

14. The seventh part of the document provides a conclusion and summary of the findings.

15. The audit has identified several areas for improvement and has provided recommendations for addressing these issues.

16. The eighth part of the document discusses the next steps in the process.

17. It is important to monitor the implementation of the recommendations and to report on progress.

18. The ninth part of the document provides a list of the documents and records that will be reviewed.

19. This list includes all documents and records that are relevant to the audit.

20. The tenth part of the document discusses the results of the audit.

21. The findings of the audit are summarized in the following table:

22. The table shows the number of errors identified in each category.

23. The eleventh part of the document provides recommendations for improving the system.

24. These recommendations are based on the findings of the audit and are intended to prevent future errors.

25. The twelfth part of the document discusses the implementation of the recommendations.

26. It is important to ensure that all staff are trained on the new procedures.

27. The thirteenth part of the document provides a conclusion and summary of the findings.

28. The audit has identified several areas for improvement and has provided recommendations for addressing these issues.

29. The fourteenth part of the document discusses the next steps in the process.

30. It is important to monitor the implementation of the recommendations and to report on progress.

31. The fifteenth part of the document provides a list of the documents and records that will be reviewed.

32. This list includes all documents and records that are relevant to the audit.

33. The sixteenth part of the document discusses the results of the audit.

34. The findings of the audit are summarized in the following table:

35. The table shows the number of errors identified in each category.

36. The seventeenth part of the document provides recommendations for improving the system.

37. These recommendations are based on the findings of the audit and are intended to prevent future errors.

38. The eighteenth part of the document discusses the implementation of the recommendations.

39. It is important to ensure that all staff are trained on the new procedures.

39. The nineteenth part of the document provides a conclusion and summary of the findings.

40. The audit has identified several areas for improvement and has provided recommendations for addressing these issues.

ELECTRICAL WORKERS
REGISTRATION BOARD

Safety • Competency

Electrical Certificate of Compliance

for a low voltage installation if prescribed electrical work has been done on any part of it and the prescribed electrical work involved placing, replacing, or repositioning conductors or fittings attached to conductors.

No. 3365162

No. of attachments

To be completed whether or not an inspection is required.**CUSTOMER INFORMATION - PLEASE PRINT CLEARLY**Name of customer STONEWOOD HOMES / FORRESTER Phone: 16-09-2010Address of installation LOT 148/28 SHERIDAN DRIVE

Postal address of customer (if not as above)

DECLARATION OF CONFORMITY (Please tick (✓) appropriate boxes)

In accordance with Regulation 58 of the Electricity (Safety) Regulations 2010, the design of the installation or part of the installation to which this certificate applies

- (a) complies with either Part 2 of AS/NZS 3000:2007 ☐ or Part 1 of AS/NZS3000:2007 and Regulation 59 ☒ and
 (b) the supply system of the installation or part of the installation to which this certificate applies is
 230V/400 V MEN ☒ or attached other system ☐

WORK DETAILS

No. of lighting outlets

No. of ranges

Please tick (✓) as appropriate where work includes:

No. of socket outlets

No. of water heaters

Mains

Main earthing system

Was any installation work carried out by the homeowner?

Yes ☒ No ☐☒ MEN Switchboard closest to point of supply

Electric lines

Description of work carried out (If necessary attach any pages with work done)

INSTALL 12 HEATPUMPS AND 12 DIS ISOLATORS
AND COMMISSION. FEED DONE BY KT ELECTRICAL

CERTIFICATION OF WORK (Please tick (✓) appropriate boxes)

I certify that the completed installation or part of the installation to which this certificate applies

- ☒ has been installed in accordance with the design detailed in the Declaration of Conformity section above
☒ has had tests which are required by the Electricity (Safety) Regulations 2010 satisfactorily completed
☒ has an earthing system that is correctly rated
☒ contains fittings which are safe to connect to a power supply
☒ is safe to connect to a power supply

ELECTRICAL WORKER DETAILSName Carl BangmaRegistration No. E254719Company ~~Carl Bangma~~ Carter ElectricContact Ph No. 021 344 988Signature Carl BangmaDate 16-9-2010**INSPECTION DETAILS**

Electrical work requiring inspection by a registered electrical inspector

☐ Mains work (mains, MEN switchboards closest to the point of supply, or main earthing systems)☐ Attached other☐ Work carried out in accordance with Part 1 of AS/NZS 3000:2007

I certify that the items identified above are electrically safe and that the inspection has been carried out in accordance with the Electricity (Safety) Regulations 2010.

Name

Registration No.

Signature

Date

Contact Ph No.

CUSTOMER COPY - THIS IS AN IMPORTANT DOCUMENT AND SHOULD BE RETAINED

CONSTRUCTION STATEMENT- PIPEWORK TESTING

SELWYN DISTRICT COUNCIL

Building Consent Number:

SOC100223

Issued by:

(Registered Craftsman Plumber)

Joseph Harris

For:

(owner)

IAN + JEANETTE FORRESTER

In respect of the testing of water pipework prior to concealment

At:

(address)

28 SHERIDAN DRIVE

I hereby state that I have personally tested the water pipework installed in the building authorised under the above Building Consent by the method indicated hereunder:

- ☒ By pressurising the pipework to 1500 kpa for a period of not less than 15 minutes for the hot and cold water supply and checking to see that there are no leaks. (NZBC G12/AS1 7.5.1 (a),(b))
- ☒ By pressurising the upvc. pipework to 1.5 times the maximum working pressure for a period of not less than 15 minutes and checking that there are no leaks. (NZBC G12/AS1 7.5.2, NZS 7643)
- ☒ By pressurising the pipework to 1500 kpa for a period of not less than 5 minutes and checking to see that there are no leaks. (NZBC G12 VM1, AS3500:Part 1.2 1998)

For sanitary fixtures used for personal hygiene, I confirm that the tempering valve has been set so as to not exceed:

☐ 45°C for early childhood centres, schools, old people's homes, institutions for people with psychiatric or physical disabilities, hospitals. (G12/AS1 6.14.1(a))

or

☒ 55°C for all other buildings. (G12/AS1 6.14.1(b))

And I believe on reasonable grounds that the pipework has passed that test.

☒ All work complies with the NZBC


I also understand that the Christchurch City Council in accepting this construction statement will be relying on it to issue the code compliance certificate at the completion of the building work.

Signature of Craftsman Plumber:

Date:

Craftsman Registration No:

Company Name:


23.7.10
16161
Signature plumbing LTD

PRODUCER STATEMENT CONSTRUCTION

ISSUED BY: Bevan McKeich Builders Ltd

TO: Selwyn District Council

IN RESPECT OF: External Cladding (Linea Weatherboard)


Bevan McKeich Builders Ltd has contracted to Stonewood Homes Ltd
(Contractor) (Employer/principal)

To carry out the above building works in accordance with the Contract titled

Lot 148 Sheridan Drive, Rolleston (new dwelling) consent 100223 ("the Contract")
(Project)

I, Bevan McKeich (*who holds Trade Certificate, Advanced Trade Certificate in carpentry, 25 years trade experience and a recognized James Hardie Installer*) a duly authorized representative of Bevan McKeich Builders Ltd believe on reasonable grounds that
(Contractor)

Bevan McKeich Builders Ltd have carried out and completed exterior cladding in accordance with the James Hardies Specifications, NZS 3604 and E2/AS1


.....
Bevan McKeich
(Signature of Authorized Agent on behalf of)

Date: 15 September 2010

Bevan McKeich Builders Ltd
(Contractor)

P O Box 69 199, Lincoln, 7640
(Address)

Electrical Certificate of Compliance

for a low voltage installation if prescribed electrical work has been done on any part of it and the prescribed electrical work involved placing, replacing, or repositioning conductors or fittings attached to conductors.

No. 3283998

No. of attachments

To be completed whether or not an inspection is required.

CUSTOMER INFORMATION - PLEASE PRINT CLEARLY

Name of customer

Mr Forester

Phone:

Address of installation

28 Sheridan Drive

Postal address of customer (if not as above)

DECLARATION OF CONFORMITY (Please tick (✓) appropriate boxes)

In accordance with Regulation 58 of the Electricity (Safety) Regulations 2010, the design of the installation or part of the installation to which this certificate applies

- (a) complies with either Part 2 of AS/NZS 3000:2007 ☒ or Part 1 of AS/NZS3000:2007 and Regulation 59 ☐ and
 (b) the supply system of the installation or part of the installation to which this certificate applies is
 230V/400 V MEN ☒ or attached other system ☐

WORK DETAILS

50 No. of lighting outlets

1

No. of ranges

40 No. of socket outlets

1

No. of water heaters

Please tick (✓) as appropriate where work includes:

☒ Mains☒ Main earthing system

Was any installation work carried out by the homeowner?

Yes

☒ No☒ MEN Switchboard☐ Electric lines

Description of work carried out (If necessary attach any pages with work done)

Insulation $\Omega = 10M\Omega$ Bonding = Pass
 Earth Continuity = 0.08 Ω Polarity = Pass
 PFC = 1.29kA Line loop = 0.17 Ω

New House as per plans.

* Mains by telepoint

* H/P By other

RCD 1 0° 180°

RCD 2 0° 180°

1 x 33.1 24.4

1 x 31.6 22.4

5 x 11.4 6.5

5 x 10.1 5.5

Ramp test = 19mA

Ramp test = 23mA

CERTIFICATION OF WORK (Please tick (✓) appropriate boxes)

I certify that the completed installation or part of the installation to which this certificate applies

☒ has been installed in accordance with the design detailed in the Declaration of Conformity section above

☒ has had tests which are required by the Electricity (Safety) Regulations 2010 satisfactorily completed

☒ has an earthing system that is correctly rated

☒ contains fittings which are safe to connect to a power supply

☒ is safe to connect to a power supply

ELECTRICAL WORKER DETAILS

Name

K.S. Electrical

Registration No.

E3428

Company

K.S. Electrical

Contact Ph No.

0274 325 327

Signature

[Signature]

Date

INSPECTION DETAILS

Electrical work requiring inspection by a registered electrical inspector

☒ Mains work (mains, MEN switchboards closest to the point of supply, or main earthing systems)

☐ Attached other

☐ Work carried out in accordance with Part 1 of AS/NZS 3000:2007

I certify that the items identified above are electrically safe and that the inspection has been carried out in accordance with the Electricity (Safety) Regulations 2010.

Name

C. Gibson

Registration No.

I241406

Signature

[Signature]

Date

16-09-10

Contact Ph No.

33 94152

1/1/2000

1/1/2000



1/1/2000

1/1/2000

1/1/2000

1/1/2000

1/1/2000

1/1/2000


1/1/2000

1/1/2000

1/1/2000

1/1/2000

1/1/2000



INSPECTION NOTICE

Inspections are to be booked by the owner or builder

Name: **STONEWOOD HOMES**

Consent No: **100223**

Site Address/Rapid No

Officer ID: AOFSTEVEG

28 SHERIDAN DRIVE, ROLLESTON

Name: Geoff Stevenson

Type of building work:

Intended Use: : 3 Bedroom Domestic Dwelling with Study & Attached Double Garage with Workshop - 300.14sqm2
DOMESTIC DWELLING

Stats Code: HOUSING - Detached Dwelling (New Dwellings Only)

On 22/09/2010 at 1:55 p.m. this site was inspected pursuant to the Building Act 2004 (section 222/230) and the Local Government Act 2004 (Section 174). The purpose of the inspection was:

INSPECTION TYPE: PRACT COMPLETION (HABITABLE)

INSPECTION RESULT: BUILDING WORK MAY NOT PROCEED/REINSPECTION REQUIRED

The Following Items are yet to be completed:

ENTERED
23/9/10

Other

1/ Provide clearance to bottom of linea panel to linea specification, master bedroom window. Install flashing & provide minimum 5mm clearance linea to flashing


Notes Summary:

Reinspection of items notice dated 19/09/10. Owner confirms item 1/ has been completed. Item 4/ still to complete.

Note: A Code Compliance Certificate is required for 2004 Building Act Consents

INSTRUCTIONS*Paul Jenkins*

Notice To:	Contractor ☐	Owner ☐	Agent ☒	Occupier
By:	Telephone ☒	Fax ☒	Posting ☐	Left on Site



INSPECTION NOTICE

Inspections are to be booked by the owner or builder

Name: **STONEWOOD HOMES**

Consent No: **100223**

Site Address/Rapid No

Officer ID: AOFSTEVEG

28 SHERIDAN DRIVE, ROLLESTON

Name: Geoff Stevenson

Type of building work:

Intended Use: : 3 Bedroom Domestic Dwelling with Study & Attached Double Garage with Workshop - 300.14sqm2
DOMESTIC DWELLING

Stats Code: HOUSING - Detached Dwelling (New Dwellings Only)

On 16/09/2010 at 2:16 p.m. this site was inspected pursuant to the Building Act 2004 (section 222/230) and the Local Government Act 2004 (Section 174). The purpose of the inspection was:

INSPECTION TYPE: PRACT COMPLETION (HABITABLE)

INSPECTION RESULT: BUILDING WORK MAY NOT PROCEED/REINSPECTION REQUIRED

The Following Items are yet to be completed:

1 Down lights Clear of insulation if not CA rated (Interior)

✓ 1/ At least one down light still to be cut clear of insulation & insulation reinstalled over kitchen area. Please check all down lights.

Sealing of Bathroom Fixtures (Interior)

✓ 2/ Seal top of tiled shower trim to walls. Both showers.

Safety Glass (Interior)

✓ 3/ Install permanent shower screens.

Other

4/ Provide clearance to bottom of linea panel to linea specification, master bedroom window.

5/ Fix all exterior heat pump units to concrete.

/complete the sealing of driveway + associated drainage

DEFERRED

Notes Summary:


Ceiling space insulation tidy. Down lights have insulation abutting. Ensure to manufactures specification. Plumbing frost protection completed. Smoke alarms installed. Sealing of wet areas completed. Safety glass installed windows. HWC seismic restraints, valving, Copper drain completed. Waste connection + venting completed. Sealing of wet areas completed. Drain venting in place. Landscaping still to complete, ensure ground levels are maintained in accordance with NZBC E2 AS1.

DOCUMENTS accepted by inspector. CCC on hold untill final has passed. 1/ Electrical energy certificate. 2/ Plumbing 1500 KPA test certificate.3/ Completed Code Compliance Application.

Note: A Code Compliance Certificate is required for 2004 Building Act Consents

INSTRUCTIONS

Notice To:	Contractor ☐	Owner ☐	Agent ☐	Occupier	
By:	Telephone ☒	Fax ☐	Posting ☐	Left on Site ☒	



INSPECTION NOTICE

Inspections are to be booked by the owner or builder

Name: **STONEWOOD HOMES**

Consent No: **100223**

Site Address/Rapid No

Officer ID: AOFBOWYET

28 SHERIDAN DRIVE, ROLLESTON

Name: Tim Bowyer

Type of building work:

Intended Use: : 3 Bedroom Domestic Dwelling with Study & Attached Double Garage with Workshop - 300.14sqm2
DOMESTIC DWELLING

Stats Code: HOUSING - Detached Dwelling (New Dwellings Only)

On 1/09/2010 at 10:37 a.m. this site was inspected pursuant to the Building Act 2004 (section 222/230) and the Local Government Act 2004 (Section 174). The purpose of the inspection was:

INSPECTION TYPE: TANKING

INSPECTION RESULT: BUILDING WORK MAY PROCEED

The Following Items are yet to be completed:

ENTERED


Notes Summary:

wet seal tanking system.showers x2 bathsplash,kick & top surface

Note: A Code Compliance Certificate is required for 2004 Building Act Consents

INSTRUCTIONS

Notice To:	Contractor ☐	Owner ☐	Agent ☐	Occupier
By:	Telephone ☐	Fax ☐	Posting ☐	Left on Site



INSPECTION NOTICE

Inspections are to be booked by the owner or builder

Name: **STONEWOOD HOMES**

Consent No: **100223**

Site Address/Rapid No

Officer ID: AOFwestwc

28 SHERIDAN DRIVE, ROLLESTON

Name: Chris Westwood

Type of building work:

Intended Use: : 3 Bedroom Domestic Dwelling with Study & Attached Double Garage with Workshop - 300.14sqm2
DOMESTIC DWELLING

Stats Code: HOUSING - Detached Dwelling (New Dwellings Only)

On 10/08/2010 at 10:02 a.m. this site was inspected pursuant to the Building Act 2004 (section 222/230) and the Local Government Act 2004 (Section 174). The purpose of the inspection was:

INSPECTION TYPE: POSTLINE

INSPECTION RESULT: BUILDING WORK MAY PROCEED

The Following Items are yet to be completed:

Notes Summary:

bathroom shower linings now screwed off at 100mm centers or less

Note: A Code Compliance Certificate is required for 2004 Building Act Consents


ENTERED

INSTRUCTIONS

Notice To: Contractor ☐ Owner ☐ Agent ☐ Occupier

By: Telephone ☐ Fax ☐ Posting ☐ Left on Site

ENTERED



INSPECTION NOTICE

Inspections are to be booked by the owner or builder

Name: **STONEWOOD HOMES**

Consent No: **100223**

Site Address/Rapid No

Officer ID: AOFSTEVEG

28 SHERIDAN DRIVE, ROLLESTON

Name: Geoff Stevenson

Type of building work:

Intended Use: : 3 Bedroom Domestic Dwelling with Study & Attached Double Garage with Workshop - 300.14sqm2
DOMESTIC DWELLING

Stats Code: HOUSING - Detached Dwelling (New Dwellings Only)

On 6/08/2010 at 9:58 a.m. this site was inspected pursuant to the Building Act 2004 (section 222/230) and the Local Government Act 2004 (Section 174). The purpose of the inspection was:

INSPECTION TYPE: POSTLINE

INSPECTION RESULT: BUILDING WORK MAY NOT PROCEED/REINSPECTION REQUIRED

The Following Items are yet to be completed:

Wet area linings to be tiled (fixed in accordance with system

/Fixing of Aqualine to bathroom to be at 100mm centre's **MAXIMUM**. Fixing presently 130mm+. Fixing in ensuit ok.

Notes Summary:


All interior linings completed Fixing of bracing panels complete. Aqualine installed in ensuit and bathroom+ laundry. Fixed for tiles in ensuit + bathroom showers Refixing in bathroom shower required. Metal corner angles installed. 10mm gib to walls 13 mm to cealings.

Note: A Code Compliance Certificate is required for 2004 Building Act Consents

INSTRUCTIONS

Notice To:	Contractor ☒	Owner ☐	Agent ☐	Occupier	
By:	Telephone ☒	Fax ☐	Posting ☐	Left on Site ☒	

*Dwain
Gib fixer*



INSPECTION NOTICE

Inspections are to be booked by the owner or builder

Name: **STONEWOOD HOMES**

Consent No: **100223**

Site Address/Rapid No

Officer ID: AOFSTEVEG

28 SHERIDAN DRIVE, ROLLESTON

Name: Geoff Stevenson

Type of building work:

Intended Use: : 3 Bedroom Domestic Dwelling with Study & Attached Double Garage with Workshop - 300.14sqm2
DOMESTIC DWELLING

Stats Code: HOUSING - Detached Dwelling (New Dwellings Only)

On 3/08/2010 at 2:46 p.m. this site was inspected pursuant to the Building Act 2004 (section 222/230) and the Local Government Act 2004 (Section 174). The purpose of the inspection was:

INSPECTION TYPE: PRELINE

INSPECTION RESULT: BUILDING WORK MAY PROCEED

The Following Items are yet to be completed:

Notes Summary:

Moisture content of frameing now less than 18%, where tested

Note: A Code Compliance Certificate is required for 2004 Building Act Consents

INSTRUCTIONS

ENTERED

Notice To:	Contractor ☐	Owner ☐	Agent ☒	Occupier	
By:	Telephone ☒	Fax ☐	Posting ☐	Left on Site ☒	

INSPECTION NOTICE

Inspections are to be booked by the owner or builder.

Name: Forrester Consent No: 100223
 Site Address/Rapid No: 28 Sheridan Drive Officer: SDC 35
Ribbton Name: Carl Green
 Type of building work: Domestic Dwelling
 On 30 / 7 / 10 at 11:48 (am/pm) this site was inspected pursuant to the
 Building Act 2004 [Section 222/230] and the Local Government Act 2004 [Section 174]. The purpose of the inspection was:-

a	Siting & Founds	h	Bond Beam	o	Other	
b	Slab	i	Blockfill	p	Resource Consent	
c	Pre Wrap	j	Heating unit	q	Complaint/investigation	
d	Post Wrap	k	Sanitary drainage	r	Compliance Schedule	
e	Half height veneer	l	Stormwater drainage	s	WOF/ c/s audit	
f	 Preline/Plumbing	m	Pile/pole holes	t	Final Inspection	☐ Pass
g	Post line bracing	n	Cladding	u		☐ Fail

BUILDING WORK MAY PROCEED ☐ MAY NOT PROCEED ☒ RE-INSPECTION YES ☒ NO ☐

INSPECTION NOTES:

Moisture check only!
 Wall frame 16.5 — 19.5%
 Bottom Plate 24 — 35%
 Moisture content remains too high
 to line. Respiration required

NOTE: A Code Compliance Certificate Application is required for 2004 Building Act Consents

Owner/Builder/Contractor confirms floor height is as recommended by Environment Canterbury ☐

INSTRUCTIONS

All work inspected is in accordance with the Building Consent ☐

Satisfactory: Work may proceed when minor items above have been attended to ☐

Some work is not satisfactory or is incomplete, as detailed above, and rectification is required. ☒

A notice to fix will be issued ☐

Notice to: Contractor ☒ Owner ☐ Agent ☐ Occupier ☐ Signed:

By: Telephone ☐ Fax ☐ Posting ☐ Left on Site ☒

ENTERED

INSPECTION NOTICE

25/01/2019

Page 1 of 1

Inspected by: [Name]

Date: 25/01/2019

Time: 10:00 AM

Location: [Address]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

Inspector: [Name]

ENTERED

Inspections are to be booked by the owner or builder.

Name: FORRESTER Consent No: 100223

Site Address/Rapid No: 28 SHONIDAN Officer: _____

DRIVE, ROLLESTON Name: SARAF

Type of building work: Swelling

On 16 / 7 / 2010 at 1520 am / pm this site was inspected pursuant to the Building Act 2004 [Section 222/230] and the Local Government Act 2004 [Section 174]. The purpose of the inspection was:-

a	Siting & Founds	h	Bond Beam	o	Other
b	Slab	i	Blockfill	p	Resource Consent
c	Pre Wrap	j	Heating unit	q	Complaint/investigation
d	Post Wrap	k	Sanitary drainage	r	Compliance Schedule
e	Half height veneer	l	Stormwater drainage	s	WOF/ c/s audit
f	Preline/Plumbing	m	Pile/pole holes	t	Final
g	Post line bracing	n	Cladding	u	Inspection
					☐ Pass
					☐ Fail

BUILDING WORK MAY PROCEED ☒ MAY NOT PROCEED ☐ RE-INSPECTION YES ☐ NO ☐

INSPECTION NOTES: Reinspection of Preline

① Moisture still 20 - 23%
 of up to 28% @ Bottom Plates
 ceiling Lined.
 Determined on 1 Heating

Rebook inspection please

ENTERED
 19/7/10

NOTE: A Code Compliance Certificate Application is required for 2004 Building Act Consents

Owner/Builder/Contractor confirms floor height is as recommended by Environment Canterbury ☐

INSTRUCTIONS

All work inspected is in accordance with the Building Consent ☐

Satisfactory: Work may proceed when minor items above have been attended to ☐

Some work is not satisfactory or is incomplete, as detailed above, and rectification is required. ☒

A notice to fix will be issued ☐

Notice to: Contractor ☒ Owner ☐ Agent ☐ Occupier ☐ Signed: _____

By: Telephone ☒ Fax ☐ Posting ☐ Left on Site ☒

INSPECTION NOTICE

Inspections are to be booked by the owner or builder.

Name: FORLESTER Consent No: 100223
 Site Address/Rapid No: 28 SHAWDAN DRIVE Officer: [Signature]
HOWESON. Name: [Signature]

Type of building work: Drainage
 On 1 / 7 / 10 at 12.30 am/pm this site was inspected pursuant to the Building Act 2004 [Section 222/230] and the Local Government Act 2004 [Section 174]. The purpose of the inspection was:-

a	Siting & Founds	h	Bond Beam	o	Other
b	Slab	i	Blockfill	p	Resource Consent
c	Pre Wrap	j	Heating unit	q	Complaint/investigation
d	Post Wrap	k	Sanitary drainage	r	Compliance Schedule
e	Half height veneer	l	Stormwater drainage	s	WOF/ c/s audit
f	☒ Preline/Plumbing	m	Pile/pole holes	t	Final ☐ Pass
g	Post line bracing	n	Cladding	u	Inspection ☐ Fail

BUILDING WORK MAY PROCEED ☐ MAY NOT PROCEED ☒ RE-INSPECTION YES ☒ NO ☐

INSPECTION NOTES: BRACE FOUNDS COMPLETED.

(B3) NEW ON KITCHEN SIDE OF WALL.

* MOVE SWITCH TO NO ELEMENT.

STRUCTURE:- 90x45 FRAME, MSC.8. H1.2 AND ORIGIN TO INTERIOR H1.2 TO EXTERIOR WALL FIXED TO SLAB, JOINTS NAKED OFF. RENDO CEILING BATTERS DIRECT @ 600 c.

* (2) MOISTURE:- 21% / 6. LP.

PLUMBING:- 3m IN GARAGE VENT TO EXISTING WC POOL BATTERY. PIPE WORK ENSURE 1500 LIA TEST. ENSURE DPM REINSTATED TO ALLOW BASES YET TO BE POURD.

THATCH:- AIR SEAL TO WINDOWS, INSULATION INSTALLED UNDER TO WALLS. R.S. BRINGS OUTS.

* (3) FIT 35x35 ANCHORS TO TIE SHOWER AREAS. ON SITE 1/6/10 ENSURE AAU TO INSTALL TO EXISTING BATH/SHOWER / KITCHEN CONFIRMATION REQ.

NOTE: A Code Compliance Certificate Application is required for 2004 Building Act Consents

Owner/Builder/Contractor confirms floor height is as recommended by Environment Canterbury ☐

INSTRUCTIONS REINSULATION ON MOISTURE AND FRAMES X MARKED

All work inspected is in accordance with the Building Consent ☐

Satisfactory: Work may proceed when minor items above have been attended to ☐

Some work is not satisfactory or is incomplete, as detailed above, and rectification is required. ☐

A notice to fix will be issued ☐

Notice to: Contractor ☒ Owner ☐ Agent ☐ Occupier ☐ Signed: [Signature]

By: Telephone ☐ Fax ☐ Posting ☐ Left on Site ☒

ENTERED

ENTERED

Building Consent Inspection Prompt Sheet Preline

PROJECT DETAILS			
Building Consent No. <u>100223</u>	Site Copy Viewed: ☒ Yes ☐ No		
Inspector's Name: <u>TJB</u>			
Time Arrived: <u>12.30</u>	Time Departed: <u>1.15</u>	Date: <u>1/7/10</u>	

ITEMS INSPECTED	
Framing	Bracing
☒ Timber species	☒ Location/type
☒ Timber grade	☒ Clear of wet areas
☒ Timber treatment	☒ Connections/fixings
☒ Moisture content	☒ Roof bracing
☒ Stud size	☒ Dragon ties
☒ Stud spacing	☒ Diaphragms
	Fixing
☒ Lintel sizes	☒ Bottom plate
☒ Post sizes	☒ Top plate
☒ Truss Layout	☒ Truss to plate
☒ Girder truss supports	☒ Purlins
☒ Ceiling batten spacing	☒ Brace bottom plate
☒ Purlins	☒ Steel angle fixings
Other	☒ Post to foundation
☒ Building wrap	☒ Post to beam
☒ Window air seals	☒ Fire walls
☒ Roof underlay	☒ Lintel
☒ DPC under plates	
☒ Insulation material	
☒ Insulation placement	
☒ Internal ventilation	
☒ Water cylinder support	
☒ Seismic restraint	
☒ Fire walls	
☒ Shower tanking	

This is not an inspection record, it serves as a prompt and simply indicates that the items listed have been inspected. The Inspection Notice provides the record of items inspected and decisions made with respect to progression of building work, together with reasons for these decisions as inspection notes.

INSPECTION NOTICE

Inspections are to be booked by the owner or builder.

Name: FORRESTER Consent No: 100223
 Site Address/Rapid No: 28 SHAWAN DRIVE Officer: [Signature]
REVESTON Name: [Signature]

Type of building work: DOCKING
 On 30 / 6 / 10 at 2.40 am / pm this site was inspected pursuant to the Building Act 2004 [Section 222/230] and the Local Government Act 2004 [Section 174]. The purpose of the inspection was:-

a	Siting & Founds	h	Bond Beam	o	Other
b	Slab	i	Blockfill	p	Resource Consent
c	Pre Wrap	j	Heating unit	q	Complaint/investigation
d	Post Wrap	k	Sanitary drainage	r	Compliance Schedule
e	Half height veneer	l	Stormwater drainage	s	WOF/ c/s audit
f	☒ Preline/Plumbing	m	Pile/pole holes	t	Final ☐ Pass
g	Post line bracing	n	Cladding	u	Inspection ☐ Fail

BUILDING WORK MAY PROCEED ☐ MAY NOT PROCEED ☒ RE-INSPECTION YES ☒ NO ☐

INSPECTION NOTES:

EXTERIOR NOT YET WATER TIGHT.
 RE-BOOK WITHIN COMPLETION

ENTERED 110

NOTE: A Code Compliance Certificate Application is required for 2004 Building Act Consents

Owner/Builder/Contractor confirms floor height is as recommended by Environment Canterbury ☐

INSTRUCTIONS

All work inspected is in accordance with the Building Consent ☐

Satisfactory: Work may proceed when minor items above have been attended to ☐

Some work is not satisfactory or is incomplete, as detailed above, and rectification is required. ☒

A notice to fix will be issued ☐

Notice to: Contractor ☒ Owner ☐ Agent ☐ Occupier ☐ Signed: [Signature]

By: Telephone ☐ Fax ☐ Posting ☐ Left on Site ☐

Inspections are to be booked by the owner or builder.

Name: Foxreston Consent No: 100223
 Site Address/Rapid No: LOT 148, 28 SHERRIDAN DRIVE, BOLLERSTON Officer: _____
 Name: DARYL
 Type of building work: AWELLING
 On 23 / 6 / 2010 at 10:15 am / pm this site was inspected pursuant to the Building Act 2004 [Section 222/230] and the Local Government Act 2004 [Section 174]. The purpose of the inspection was:-

a	Siting & Founds	h	Bond Beam	o	☒ Other
b	Slab	i	Blockfill	p	Resource Consent
c	Pre Wrap	j	Heating unit	q	Complaint/investigation
d	Post Wrap	k	Sanitary drainage	r	Compliance Schedule
e	Half height veneer	l	Stormwater drainage	s	WOF/ c/s audit
f	Preline/Plumbing	m	Pile/pole holes	t	Final
g	Post line bracing	n	Cladding	u	Inspection
					☐ Pass
					☐ Fail

BUILDING WORK MAY PROCEED ☒ MAY NOT PROCEED ☐ RE-INSPECTION YES ☐ NO ☒

INSPECTION NOTES:

- Cavity Battens
- 40 x 20 H3.1 Cavity Battens within 600%
 - Cavity Closers in Place
 - INTERNAL CORNER U.P.V.C. FLASHINGS in Place
 - INTERNAL CORNER FLASHING @ CLADDING CHANGE (METAL)
 - SOAKERS TO EXTERNAL CORNERS TO BE USED (METAL)

EXTENDED

NOTE: A Code Compliance Certificate Application is required for 2004 Building Act Consents

Owner/Builder/Contractor confirms floor height is as recommended by Environment Canterbury ☐

INSTRUCTIONS

All work inspected is in accordance with the Building Consent ☒

Satisfactory: Work may proceed when minor items above have been attended to ☐

Some work is not satisfactory or is incomplete, as detailed above, and rectification is required. ☐

A notice to fix will be issued ☐

Notice to: Contractor ☒ Owner ☐ Agent ☐ Occupier ☐ Signed: _____

By: Telephone ☐ Fax ☐ Posting ☐ Left on Site ☒

NOTICE (3)


1. NAME		2. ADDRESS	
3. CITY		4. STATE	
5. ZIP		6. PHONE	
7. OCCUPATION		8. EDUCATION	
9. MARITAL STATUS		10. NUMBER OF CHILDREN	
11. DATE OF BIRTH		12. DATE OF DEATH	
13. DATE OF BURIAL		14. DATE OF CREMATION	
15. DATE OF INTERMENT		16. DATE OF REINTERMENT	
17. DATE OF EXHUMATION		18. DATE OF REINTERMENT	
19. DATE OF REINTERMENT		20. DATE OF REINTERMENT	
21. DATE OF REINTERMENT		22. DATE OF REINTERMENT	
23. DATE OF REINTERMENT		24. DATE OF REINTERMENT	
25. DATE OF REINTERMENT		26. DATE OF REINTERMENT	
27. DATE OF REINTERMENT		28. DATE OF REINTERMENT	
29. DATE OF REINTERMENT		30. DATE OF REINTERMENT	
31. DATE OF REINTERMENT		32. DATE OF REINTERMENT	
33. DATE OF REINTERMENT		34. DATE OF REINTERMENT	
35. DATE OF REINTERMENT		36. DATE OF REINTERMENT	
37. DATE OF REINTERMENT		38. DATE OF REINTERMENT	
39. DATE OF REINTERMENT		40. DATE OF REINTERMENT	
41. DATE OF REINTERMENT		42. DATE OF REINTERMENT	
43. DATE OF REINTERMENT		44. DATE OF REINTERMENT	
45. DATE OF REINTERMENT		46. DATE OF REINTERMENT	
47. DATE OF REINTERMENT		48. DATE OF REINTERMENT	
49. DATE OF REINTERMENT		50. DATE OF REINTERMENT	
51. DATE OF REINTERMENT		52. DATE OF REINTERMENT	
53. DATE OF REINTERMENT		54. DATE OF REINTERMENT	
55. DATE OF REINTERMENT		56. DATE OF REINTERMENT	
57. DATE OF REINTERMENT		58. DATE OF REINTERMENT	
59. DATE OF REINTERMENT		60. DATE OF REINTERMENT	
61. DATE OF REINTERMENT		62. DATE OF REINTERMENT	
63. DATE OF REINTERMENT		64. DATE OF REINTERMENT	
65. DATE OF REINTERMENT		66. DATE OF REINTERMENT	
67. DATE OF REINTERMENT		68. DATE OF REINTERMENT	
69. DATE OF REINTERMENT		70. DATE OF REINTERMENT	
71. DATE OF REINTERMENT		72. DATE OF REINTERMENT	
73. DATE OF REINTERMENT		74. DATE OF REINTERMENT	
75. DATE OF REINTERMENT		76. DATE OF REINTERMENT	
77. DATE OF REINTERMENT		78. DATE OF REINTERMENT	
79. DATE OF REINTERMENT		80. DATE OF REINTERMENT	
81. DATE OF REINTERMENT		82. DATE OF REINTERMENT	
83. DATE OF REINTERMENT		84. DATE OF REINTERMENT	
85. DATE OF REINTERMENT		86. DATE OF REINTERMENT	
87. DATE OF REINTERMENT		88. DATE OF REINTERMENT	
89. DATE OF REINTERMENT		90. DATE OF REINTERMENT	
91. DATE OF REINTERMENT		92. DATE OF REINTERMENT	
93. DATE OF REINTERMENT		94. DATE OF REINTERMENT	
95. DATE OF REINTERMENT		96. DATE OF REINTERMENT	
97. DATE OF REINTERMENT		98. DATE OF REINTERMENT	
99. DATE OF REINTERMENT		100. DATE OF REINTERMENT	

Building Consent Inspection Prompt Sheet Cladding/Envelope

PROJECT DETAILS			
Building Consent No.	100223	Site Copy Viewed:	☒ Yes ☐ No
Inspector's Name:	D. Forster		
Time Arrived:	Time Departed:	Date: 23/6/10	

ITEMS INSPECTED	
☒ Cavity Width 20mm	☒ System
☒ Ties	☒ Wrap/Ridged Barrier
☒ Tie Spacing	☐ Sill Flashing
☐ Brick Type	☐ Head Flashing
☐ Bottom Ties	☐ Jamb Flashing
☐ Clean Cavity	☐ Netting
☐ Steel Lintels	☐ Control Joints
☐ Weep Holes	☒ Vermin Proofing
☐ Panel Width	☐ Air Seals
☐ Jointing	☐ Backing Materials
☒ Cavity Closed to Ceiling	☐ Internal Gutters
☐ Penetrations	☐ Sub Strate Fixing
	☐ Thermal Barrier

This is not an inspection record; it serves as a prompt and simply indicates that the items listed have been inspected. The Inspection Notice provides the record of items inspected and decisions made with respect to progression of building work, together with reasons for these decisions as inspection notes.




INSPECTION NOTICE

Inspections are to be booked by the owner or builder

Name: STONEWOOD HOMES	Consent No: 100223
Site Address/Rapid No	Officer ID: AOFroberp
28 SHERIDAN DRIVE, ROLLESTON	Name: Peter Robertson
Type of building work:	
Intended Use: : 3 Bedroom Domestic Dwelling with Study & Attached Double Garage with Workshop - 300.14sqm2 DOMESTIC DWELLING	
Stats Code: HOUSING - Detached Dwelling (New Dwellings Only)	
On 18/06/2010 at 9:11 a.m. this site was inspected pursuant to the Building Act 2004 (section 222/230) and the Local Government Act 2004 (Section 174). The purpose of the inspection was:	
INSPECTION TYPE: HALF HIGH BRICK	
INSPECTION RESULT: BUILDING WORK MAY PROCEED	

The Following Items are yet to be completed:

Notes Summary:				
●ck ties 2nd up then every 4th thereafter,brick ties 300mm centres up openings ,40mm cavity wash outs in place small amount of brick work to start approx 3m inlength profiles set up for 40mm cavity may proceed and ensure to same standard as inspected,Cavity battens yet to be installed and inspected.				
Note: A Code Compliance Certificate is required for 2004 Building Act Consents				
INSTRUCTIONS				
ENTERED				
Notice To:	Contractor ☐	Owner ☐	Agent ☐	Occupier



INSPECTION NOTICE

Inspections are to be booked by the owner or builder

Name: **STONEWOOD HOMES**

Consent No: **100223**

Site Address/Rapid No

Officer ID: AOFroberp

28 SHERIDAN DRIVE, ROLLESTON

Name: Peter Robertson

Type of building work:

Intended Use: : 3 Bedroom Domestic Dwelling with Study & Attached Double Garage with Workshop - 300.14sqm2
DOMESTIC DWELLING

Stats Code: HOUSING - Detached Dwelling (New Dwellings Only)

On 18/06/2010 at 9:06 a.m. this site was inspected pursuant to the Building Act 2004 (section 222/230) and the Local Government Act 2004 (Section 174). The purpose of the inspection was:

INSPECTION TYPE: PRE-CLADDING

INSPECTION RESULT: BUILDING WORK MAY PROCEED

The Following Items are yet to be completed:

Notes Summary:

Items from inspection dated 11/06/10 have been completed except for item 2 being cavity battens.

Note: A Code Compliance Certificate is required for 2004 Building Act Consents

INSTRUCTIONS

ENTERED

Notice To:

Contractor ☐

Owner ☐

Agent ☐

Occupier

By:

Telephone ☐

Fax ☐

Posting ☐

Left on Site

INSPECTION NOTICE

Inspections are to be booked by the owner or builder.

Name: I+J Forrester Consent No: 100223
 Site Address/Rapid No: 28 Sheridan Drive Officer: _____
Rollerton Name: Geoff Stevenson

Type of building work: Domestic Dwellling

On 11 / 06 / 10 at 8-42 am / pm this site was inspected pursuant to the Building Act 2004 [Section 222/230] and the Local Government Act 2004 [Section 174]. The purpose of the inspection was:-

a	Siting & Founds	h	Bond Beam	o	Other
b	Slab	i	Blockfill	p	Resource Consent
c	Pre Wrap	j	Heating unit	q	Complaint/investigation
d	☒ Post Wrap	k	Sanitary drainage	r	Compliance Schedule
e	Half height veneer	l	Stormwater drainage	s	WOF/ c/s audit
f	Preline/Plumbing	m	Pile/pole holes	t	Final ☐ Pass
g	Post line bracing	n	Cladding	u	Inspection ☐ Fail

BUILDING WORK MAY PROCEED ☒ MAY NOT PROCEED ☐ RE-INSPECTION ☒ YES ☐ NO ☐

INSPECTION NOTES:

- * 1/ ☒ Items from last inspection 4-06-10 still to complete (CPC40, Joist hangers + roof bracing + web bracing)
- x 2/ Cavity battens still to install.
 Tyvek wrap stapled to exterior framing. Flashing tape fixed to exterior corners.
- x 3/ Flash tape may need to be heated to ensure ~~being~~ ~~to wrap~~ a seal to wrap is achieved. Wrap cut clear of foundation. DPM turned up at slab edge, penetrations taped. Mohe box in place flash taped to wrap. Exterior joinery, flashings, + support bars still to install.
- x 4/ Install ext joinery. Flashings + support bars.
 Reinspection required for above items. 1 to 4.
 7.5m easterly diaphan installed at entry. Fixed 150 g

ENTERED

NOTE: A Code Compliance Certificate Application is required for 2004 Building Act Consents

Owner/Builder/Contractor confirms floor height is as recommended by Environment Canterbury ☐

INSTRUCTIONS

All work inspected is in accordance with the Building Consent ☐

Satisfactory: Work may proceed when minor items above have been attended to ☒

Some work is not satisfactory or is incomplete, as detailed above, and rectification is required. ☒

A notice to fix will be issued ☐

Notice to: Contractor ☒ Owner ☐ Agent ☐ Occupier ☐ Signed: _____
 By: Telephone ☐ Fax ☐ Posting ☐ Left on Site ☐

INSPECTION NOTED

DATE		TIME		LOCATION		REMARKS	

Building Consent Inspection Prompt Sheet Post-Wrap

PROJECT DETAILS			
Building Consent No. <u>100223</u>	Site Copy Viewed: ☒ Yes ☐ No		
Inspector's Name: <u>Geoff Stevenson</u>			
Time Arrived: <u>8-42 AM</u>	Time Departed:	Date: <u>11-06-10</u>	

ITEMS INSPECTED			
Framing			
☒	Wrap to foundation <u>cut clear</u>	☒	<u>Flashing tape to extension openings</u>
☒	Wrap fixing	☒	<u>DPM Turned up at slab edge</u>
☒	Wrap condition/type <u>Tyvek</u>		
☒	Window flashings <u>to install</u>		
☒	Penetration seals <u>at inspection</u>		

This is not an inspection record, it serves as a prompt and simply indicates that the items listed have been inspected. The Inspection Notice provides the record of items inspected and decisions made with respect to progression of building work, together with reasons for these decisions as inspection notes.

cavity Battens

- x Items from last inspec. still to complete.
- x Ensure Flash tape is sealed to wrap. Heat gun may be reqd
- x cavity battens still to install

INSPECTION NOTICE

Inspections are to be booked by the owner or builder.

Name: Forrester Consent No: 100223
 Site Address/Rapid No: 28 Sheridan drive Officer: 27
rolleston Name: Chris Westwood

Type of building work: Dwelling
 On 4 / 6 / 10 at 8.24 am / pm this site was inspected pursuant to the Building Act 2004 [Section 222/230] and the Local Government Act 2004 [Section 174]. The purpose of the inspection was:-

a	Siting & Founds	h	Bond Beam	o	Other
b	Slab	i	Blockfill	p	Resource Consent
c	☒ Pre Wrap	j	Heating unit	q	Complaint/investigation
d	Post Wrap	k	Sanitary drainage	r	Compliance Schedule
e	Half height veneer	l	Stormwater drainage	s	WOF/ c/s audit
f	Preline/Plumbing	m	Pile/pole holes	t	Final ☐ Pass
g	Post line bracing	n	Cladding	u	Inspection ☐ Fail

BUILDING WORK MAY PROCEED ☒ MAY NOT PROCEED ☐ RE-INSPECTION YES ☐ NO ☒

INSPECTION NOTES:

Plans on site

90x45 MSg.8 Oregon at 400x with DPC under M3
bottom plate: Partials 3x2 & fixed for High wind

Ply bracing fixed off with 8/s nails

Entrance way Diaphragm in place

Bottom plate connections complete

lintel connections complete

Stud to top plate connections complete

1/ top plate to bruss internal connection to complete
marked on as built

2/ web bracing to complete

3/ Roof bracing to complete

ENTERED
4/6/10


NOTE: A Code Compliance Certificate Application is required for 2004 Building Act Consents

Owner/Builder/Contractor confirms floor height is as recommended by Environment Canterbury ☐

INSTRUCTIONS

All work inspected is in accordance with the Building Consent ☐

Satisfactory: Work may proceed when minor items above have been attended to 1/ 2.1 & 3.1 ☒

Some work is not satisfactory or is incomplete, as detailed above, and rectification is required. ☐

A notice to fix will be issued ☐

Notice to: Contractor ☒ Owner ☐ Agent ☐ Occupier ☐ Signed: 
 By: Telephone ☐ Fax ☐ Posting ☐ Left on Site ☒

Building Consent Inspection Prompt Sheet Pre-Wrap

PROJECT DETAILS			
Building Consent No.	100223	Site Copy Viewed:	☒ Yes ☐ No
Inspector's Name:	Chris		
Time Arrived:	8.24	Time Departed:	9.36
		Date:	1/6/10

ITEMS INSPECTED	
Framing	Bracing
☒ Timber species <i>Oregon</i>	☒ Location/type
☒ Timber grade <i>M3088</i>	☒ Fixings (ply)/connections
☒ Timber treatment <i>M3 bottom plate</i>	☒ Roof bracing <i>to R/L</i>
☒ Stud sizes <i>90 x 45</i>	☒ Dragon ties
☒ Stud spacings <i>400 &</i>	Fixings
☐ Lintel sizes	☒ Bottom plate
☐ Post sizes	☒ Top plate
☒ Truss layout	☒ Truss to plate
☒ Girder truss supports <i>To complete internal</i>	☒ Purlins <i>M3088</i>
☒ Purlin sizes <i>8 x 2</i>	☒ Lintel
☒ DPC under plates	☒ Steel angles
	☒ Fire walls

This is not an inspection record, it serves as a prompt and simply indicates that the items listed have been inspected. The Inspection Notice provides the record of items inspected and decisions made with respect to progression of building work, together with reasons for these decisions as inspection notes.

entrance diaphragm in place
Wardie nailed off at 150 & around
perimeter.

31 Sonter Road
P O Box 11-178
Sockburn
Christchurch 8443



Ph. 348-3401
Fax 348-3402
Email: sales@westlake.co.nz
www.westlake.co.nz

AS BUILT DOCUMENTATION

1 of 8

DATE: 12/5/10

WITH REGARDS TO CONSENT NO

100223

Westlake Timber Ltd can confirm that the above project has been fabricated and supplied in accordance with the previously submitted AGREEMENT LETTER.

Please find attached the following.

- 1: As built truss layout and producer statement.
2. Truss to truss and truss to top plate fixings.
3. Stud to top plate and lintel fixings.

Additional information:

Please make this information available to your inspectors for their on site inspection visits.

**CHRIS RANDALL
MANAGER
WESTLAKE TIMBER LTD**

Inspection
File

100223

12 MAY 2010

240551357148
V3

Westlake Timber

Producer Statement : Page 1

Job: 10-110

Client: A Customer
Phone:Site: Stonewood Homes
28 Sheridan Dr
RollestonDescription:
Building Consent No.:
MITek 20/20 Engineering 4.5.100Phone:
Printed 17:09:09 11 May 2010**PRODUCER STATEMENT for MITek 20/20™ TRUSS DESIGN**

The MITek 20/20™ truss design program has been developed by MITek New Zealand Ltd for the design of GANG-NAIL® timber roof, floor and attic trusses in New Zealand. The truss designs computed by MITek 20/20™ are prepared using sound and widely accepted engineering principles, and in accordance with compliance documents of the New Zealand Building Code and Verification Method B1/VM1; and internationally accepted standard ANSI/TPI 1 - 2002 as an alternative solution to satisfy the requirements of Clause B1 of the Building Code.

This producer statement covers the MITek 20/20™ truss design and the structural performance of the GANG-NAIL plate.

On behalf of MITek New Zealand Ltd, and subject to:

- All proprietary products meeting their performance specification requirements
- The provision of adequate roof bracing and overall building stability
- Correct selection and placement of fixings
- Correct input of Truss Design Data below
- The design being undertaken by suitably trained personnel
- The truss design being carried out in accordance with MITek 20/20 User Terms and Conditions.

I believe on reasonable grounds that the trusses, if constructed in accordance with the MITek 20/20™ truss design and shop drawings, will comply with the relevant provisions of the Building Code.

MITek New Zealand Ltd holds a current policy of Professional Indemnity Insurance no less than \$500,000.

On behalf of MITek New Zealand Ltd,

In Ling Ng, BE (Hons), CPEng, IntPE, MIPENZ (ID: 146585)
TECHNICAL SERVICES MANAGER, MITek New Zealand Ltd

MITek 20/20™ TRUSS DESIGN DATA

The MITek 20/20™ computer design for this job is based on the following design parameters entered into the program. The GANG-NAIL Fabricator shall ensure that these job details are current and relevant to the project for the design of the trusses.

Job Details**Roof Truss**

Timber Group: ~MSGx45 CF

Roof

Material: Galv Iron .5mm
Dead Load: 0.210 kPa
Restraints: 900 mm centres
Live Load: Q_{ur} = 0.250 kPa
Q_c = 1.100 kN

Importance Level: 2

Pitch: 25.000 deg

Ceiling

Material: Standard
Dead Load: 0.200 kPa
Restraints: 400 mm centres
Live Load: Q_c = 1.400 kN

Design Working Life: 50 years

Std Overhang: 600 mm

Wind

Area: High (44.0 m/s)
Pressure Coeff: C_{pe} = varies; C_{pi} = -0.30, 0.20

Snow

Location: Christchurch (N4 at 100 m)
Open Ground Load: 0.900 kPa
Basic Roof Load: 0.441 kPa

The timber for these trusses shall be standard gauged and treated to the requirements of NZS 3602:2003. Unless otherwise noted, this design assumes that the steel fixings and timber connectors proposed are located in a "closed environment", as defined by NZS3604:1999 Section 4.

Truss List

Legend: * = detail only, ? = input only, Fxx = failed design, Ø = non certified, Unmarked trusses = designed successfully, LB = lateral bracing required

Truss	Qty	Span (mm)	Pitch (deg)	Spacing (mm)	Truss	Qty	Span (mm)	Pitch (deg)	Spacing (mm)	Truss	Qty	Span (mm)	Pitch (deg)	Spacing (mm)
J03B	1	3025	25.000	900	J01B	1	2267	25.000	900	J12A	1	1372	25.000	900
J03C	1	3025	25.000	900	J02	1	1367	25.000	900	J12B	1	1372	25.000	900
J06D	1	2617	25.000	900	J02A	1	1367	25.000	900	J12C	1	1372	25.000	900
J13D	1	2522	25.000	900	J02B	1	1367	25.000	900	J13	1	2522	25.000	900
J13F	1	2522	25.000	900	J02C	1	1367	25.000	900	J13A	1	2522	25.000	900
J13H	1	2522	25.000	900	J03	1	3025	25.000	900	J13B	1	2522	25.000	900
J13M	1	2522	25.000	900	J03A	1	3025	25.000	900	J13C	1	2522	25.000	900
J13N	1	2522	25.000	900	J03D	1	3025	25.000	900	J13E	1	2522	25.000	900
J13O	1	2522	25.000	900	J04	1	2125	25.000	900	J13G	1	2522	25.000	900
J13P	1	2522	25.000	900	J04A	1	2125	25.000	900	J13I	1	2522	25.000	900
PTG011		7218	0.000	900	J05	1	1225	25.000	900	J13J	1	2522	25.000	900
T01	1	4580	25.000	900	J05A	1	1225	25.000	900	J13K	1	2522	25.000	900
T02	2	7080	25.000	900	J06	1	2617	25.000	900	J13L	1	2522	25.000	900
T04	1	4590	25.000	900	J06A	1	2617	25.000	900	J14	1	1622	25.000	900
T04A	1	4590	25.000	900	J06B	1	2617	25.000	900	J14A	1	1622	25.000	900
T06	1	6070	25.000	900	J06C	1	2617	25.000	900	T03	1	6070	25.000	900
T13	1	8970	25.000	900 LB	J06E	1	2617	25.000	900	T05	1	6070	25.000	900
T14	1	8970	25.000	900	J06F	1	2617	25.000	900	T07	3	10000	25.000	900
T15	1	9570	25.000	900	J07	1	1717	25.000	900	T08	3	4580	25.000	726
T16	1	14090	25.000	900 LB	J07A	2	1717	25.000	900	T09	4	4610	25.000	900
T16A	1	14090	25.000	900 LB	J07B	2	1717	25.000	900	T10	2	4610	25.000	811
T17	1	6080	25.000	900	J07C	1	1717	25.000	900	T11	1	3330	25.000	798
T21	1	9835	25.000	900	J08	1	3012	25.000	900	T11A	1	3330	25.000	798
TG01	1	10000	25.000	900	J08A	1	3012	25.000	900	T12	1	3330	25.000	798
TG02	1	10000	25.000	900	J09	1	2112	25.000	900	T18	1	6080	25.000	900
TG03	1	7080	25.000	900	J09A	1	2112	25.000	900	T19	1	6080	25.000	900
TG03A	1	7080	25.000	900	J10	1	1212	25.000	900	T20	1	9835	25.000	900
TR02	1	14090	25.000	900	J10A	1	1212	25.000	900	TR01	1	5210	25.000	900
TR03	1	14090	25.000	900 LB	J11	1	2272	25.000	900	TR04	1	14090	25.000	900
TR03A	1	14090	25.000	900 LB	J11A	1	2272	25.000	900	V01	1	2370	25.000	900
J01	1	2267	25.000	900	J11B	1	2272	25.000	900	V02	1	1515	25.000	900
J01A	1	2267	25.000	900	J12	1	1372	25.000	900	V03	1	1539	25.000	900

Inspection
File

100223

12 MAY 2010

Westlake Timber

Producer Statement : Page 1

Job: 10-110

Client: A Customer
Phone:

Site: Stonewood Homes
28 Sheridan Dr
Rolleston

Description:
Building Consent No.:
MITek 20/20 Engineering 4.5.160


MITek New Zealand Ltd

Phone: Printed: 17:08:09 11 May 2010

Truss	Qty	Span (mm)	Pitch (deg)	Spacing (mm)	Truss	Qty	Span (mm)	Pitch (deg)	Spacing (mm)	Truss	Qty	Span (mm)	Pitch (deg)	Spacing (mm)
V04	1	1769	25.000	900	*HB03	1	7843	18.249	900	*R02A	6	913	25.000	900
V05	1	869	25.000	900	*HB04	3	5778	18.249	900	*R02B	1	913	25.000	900
V06	1	3980	25.000	900	*HB05	1	1229	18.249	900	*R03	1	1953	25.000	900
V07	1	2990	25.000	856	*HB06	1	5064	18.249	900	*R04	1	938	25.000	900
V08	1	1278	25.000	856	*HB07	1	1080	18.249	900	*R05	1	1430	25.000	900
V09	1	2178	25.000	900	*HB08	2	4017	18.249	900	*R05A	2	1430	25.000	900
V10	1	1530	25.000	900	*HB09	1	10735	18.249	900	*R06	1	901	25.000	900
V11	1	2497	25.000	900	*HB10	1	3647	18.249	900	*R07	1	925	25.000	900
V12	1	1597	25.000	900	*HB11	1	6185	18.249	900	*R08	1	1085	25.000	900
V13	1	697	25.000	900	*HB12	1	6361	18.249	900	*R08A	1	1085	25.000	900
V14	2	2271	25.000	170	*R01	1	1080	25.000	900	*R09	1	4530	25.000	900
*HB01	2	4010	18.249	900	*R01A	1	1080	25.000	900	*R10	1	1335	25.000	900
*HB02	1	3756	18.249	900	*R02	6	913	25.000	900	*R11	1	1070	25.000	900

Total quantity : 162

The computer design input has been carried out by:

Signed: 

Date: 11-05-2010

Name of Computer Operator: Matt Linton

Qualifications and Title: Designer

Company: Westlake Timber

Verification / Acceptance of Input Data:

I have checked the input data against the construction drawings and specifications and verify that they are correct and suitable for this job.

Signed: _____

Date: _____

Name: _____


Company: _____

Inspection
File


100223

12 MAY 2010


T13




T16




T16A



TR03




TR03A



These trusses require
web bracing as shown

NO SLAB THICKENING REQUIRED FROM TRUSS LOADS



★ PRENAIL FRAMES★ TRUSSES★ TIMBER

31 Senter Road, Wigram Phone (03) 348-3401
P.O. Box 16 737 Fax (03) 348-3402
Christchurch Email: sales@westlake.co.nz

Job Name: Stonewood Homes _ Forrester

Address: 28 Sheridan Dr, Rolleston

Job: 10-110 Page 2 of 6

Scale: 1:150 Date: 08/05/2010 Drawn By: Matt Lintott

**Inspection
File**

100223

SELWYN DISTRICT COUNCIL
[Signature] 13/5/10
CONSENT DOCUMENT

12 MAY 2010



Scale 1:150 Date 08/05/2010 Drawn By Matt Linton


Inspection File

100223

SELWYN DISTRICT COUNCIL

13/5/10
CONSENT DOCUMENT

12 MAY 2010

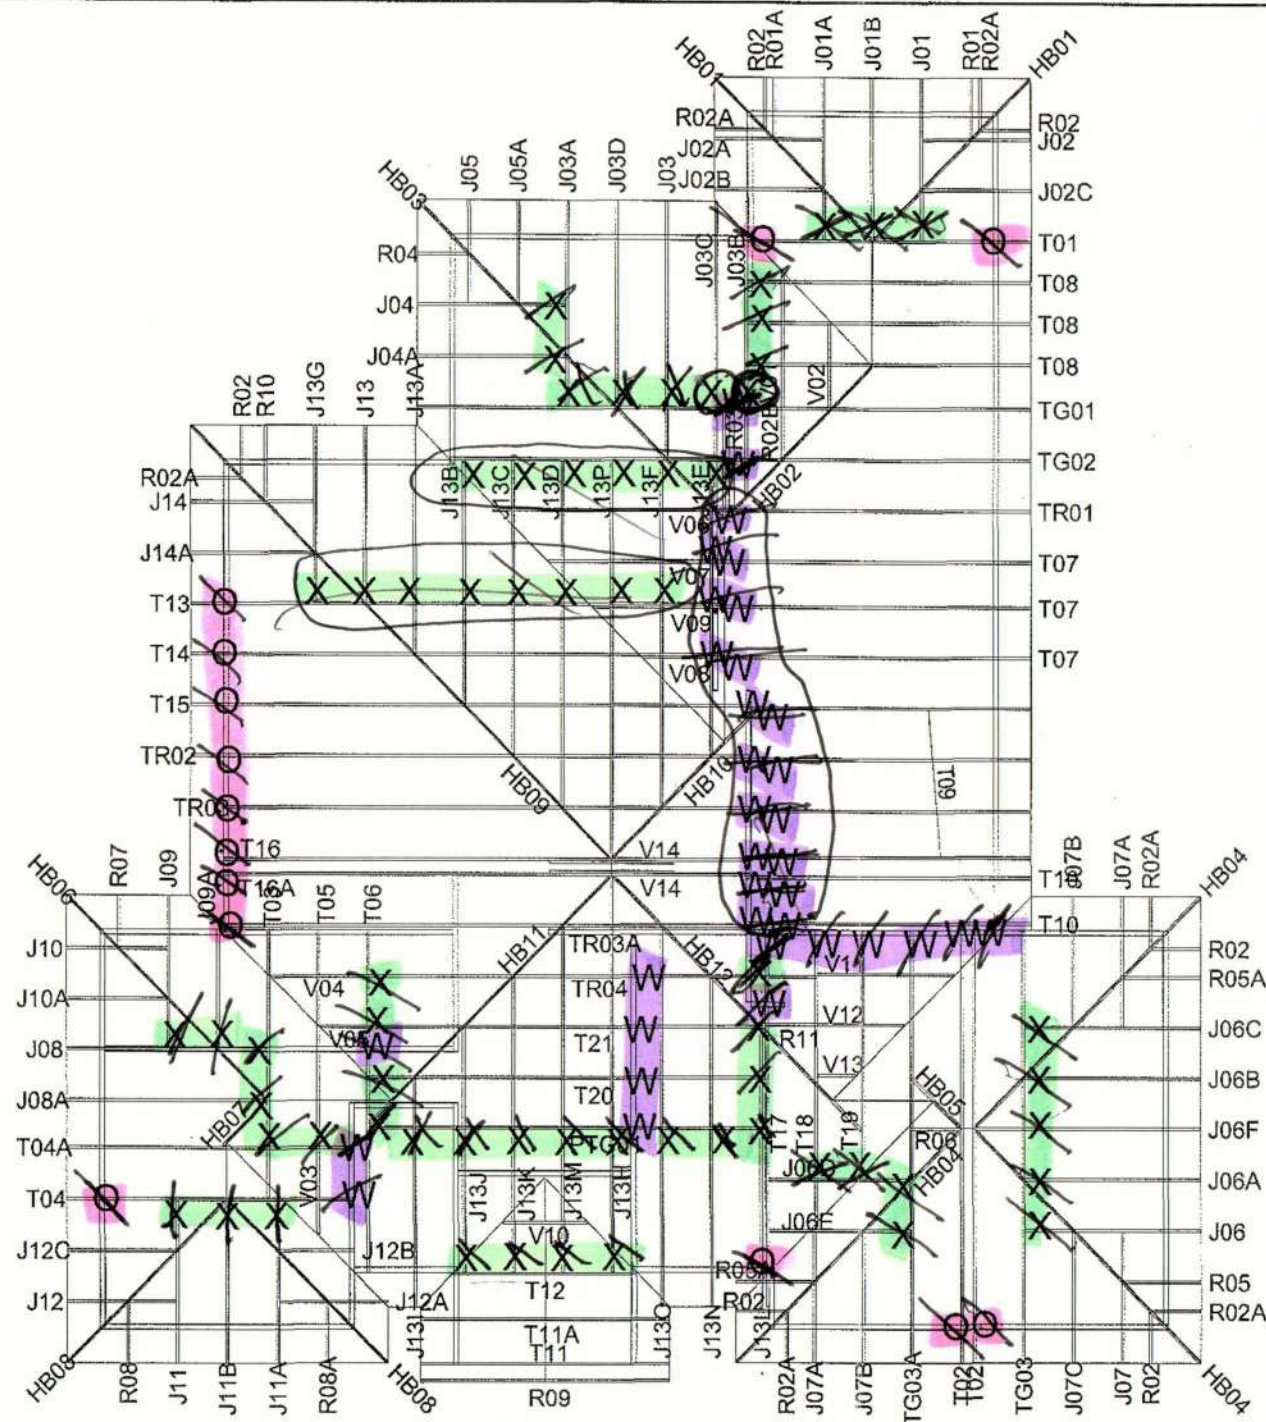

AS BUILT LAYOUT
ALL TIMBER TREATMENT COMPLIES WITH THE REQUIREMENTS OF THE BUILDING CONSENT ISSUED

WESTLAKE TIMBER LTD

★ PRENAIL FRAMES★ TRUSSES★ TIMBER

31 Senter Road, Wigram Phone (03) 348-3401
P.O. Box 16 737 Fax (03) 348-3402
Christchurch Email: sales@westlake.co.nz

Job Name: Stonewood Homes - Forrester

Address: 28 Sheridan Dr, Rolleston

10-110 Page 5 of 6

Scale: 1:150 Date: 08/05/2010 Drawn By: Matt Lindott

FIXINGS:

- Wire Dogs supplied for all truss to plate fixing
- X - Denotes 90x47 joist hanger
- Z - Denotes 120x47 joist hanger
- P - Denotes 190x47 joist hanger
- E - Denotes 165x95 joist hanger
- O - Denotes a pair of CT200 ceiling ties
- M - Denotes multigrip each side
- N - Denotes nailon plate
- W - Denotes Pair of CPC40 Cleats
- K - Denotes Pair of CPC80 Cleats
- ALL THE ABOVE UNITS MUST BE FULLY NAILED

Please Note:

Builder Should Ensure That ALL OSH Approved Safety Practices Are Carried Out When Erecting Wall & Roof Framing.

Builder To Read Pre-Cut Plans in Conjunction With Architectural Plans. Builder To Check All Opening Trim Sizes And Braces On Site Before Enclosing. If Any Difference Contact Westlake Timber Ltd.

Westlake Timber Ltd Will Not Accept Any Charges For Remedial Work Unless Written Authority Is Issued By Westlake Timber Ltd Before Work Is Commenced. A Copy Of The Order Is To Accompany Any Invoice To Westlake Timber Ltd.

If Experiencing Problems, Contact: Westlake Timber Ltd

**Inspection
File**


100223

SELWYN DISTRICT COUNCIL

13/5/10

CONSENT DOCUMENT

12 MAY 2010

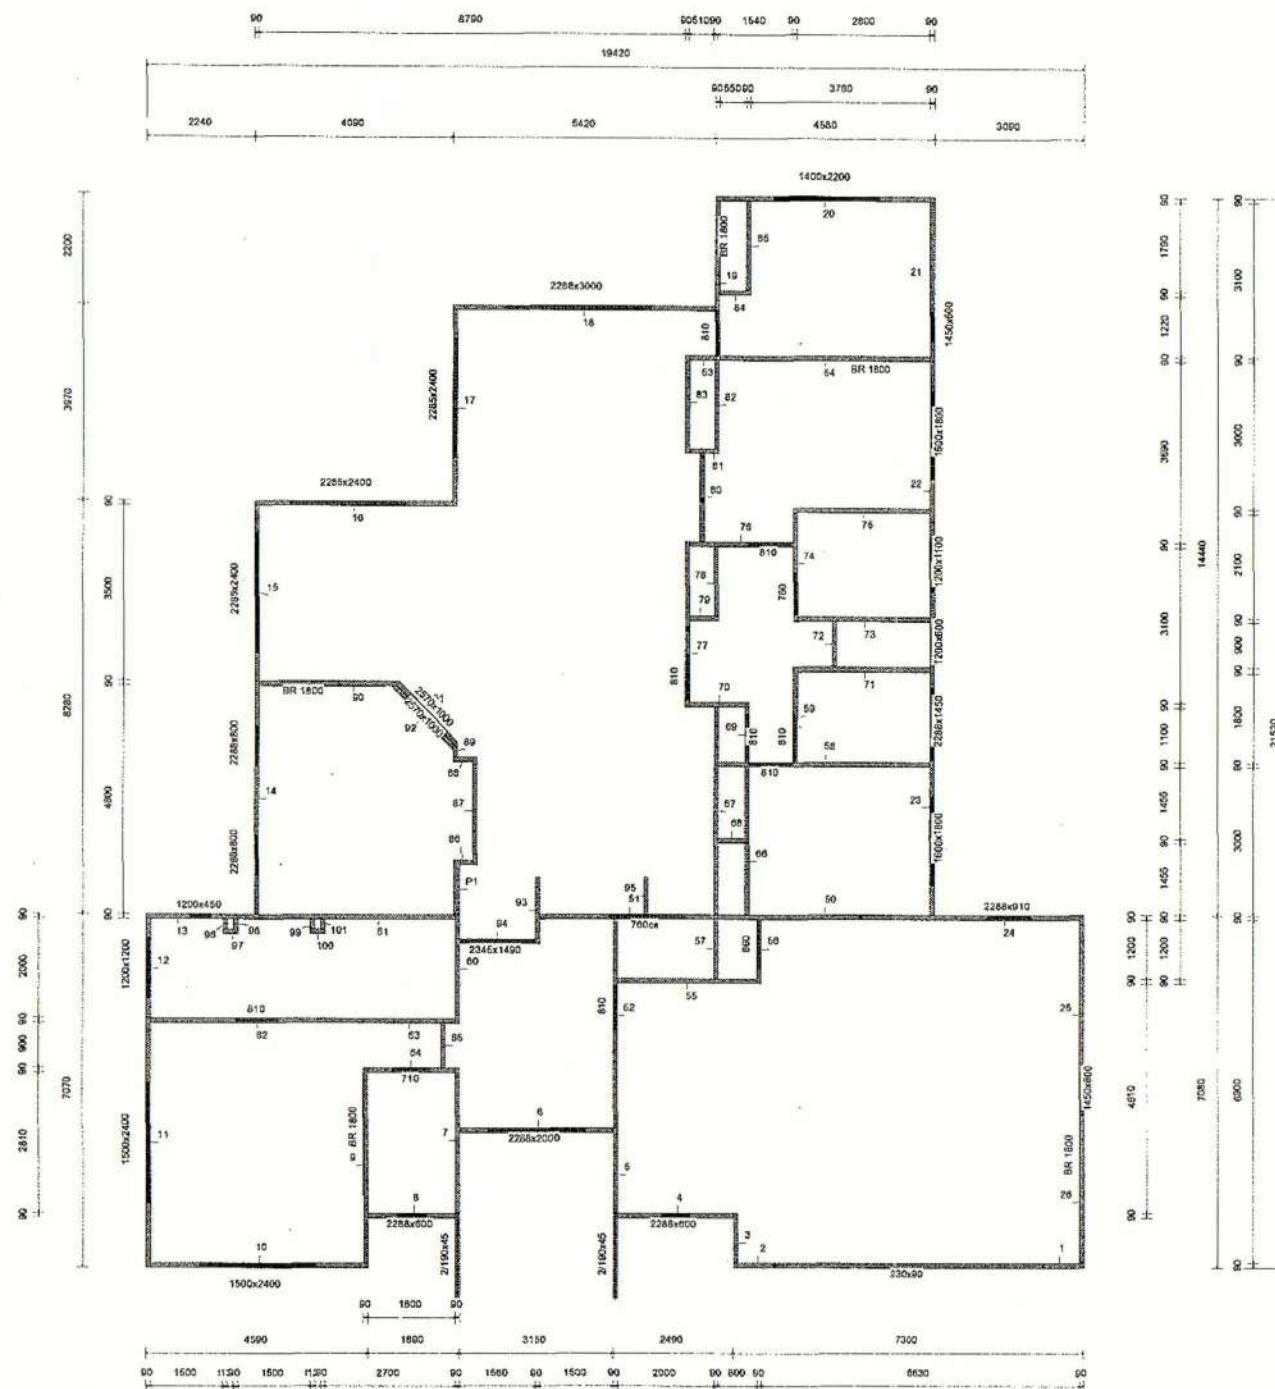

AS BUILT LAYOUT
ALL TIMBER TREATMENT COMPLIES WITH THE REQUIREMENTS OF THE BUILDING CONSENT ISSUED



★ PRENAIL FRAMES★ TRUSSES★ TIMBER

31 Souter Road, Wigram Phone (03) 348-3401
P.O. Box 16 737 Fax (03) 348-3402
Christchurch Email: sales@westlake.co.nz

Job Name Stonewood Homes - Forrester

Address 28 Sheridan Dr, Rolleston


Job 10-110 Page 3 of 6
Scale 1:150 Date 08/05/2010 Drawn By Matt Lintott

**Inspection
File**

100223

SELWYN DISTRICT COUNCIL
13/5/10
CONSENT DOCUMENT

12 MAY 2010

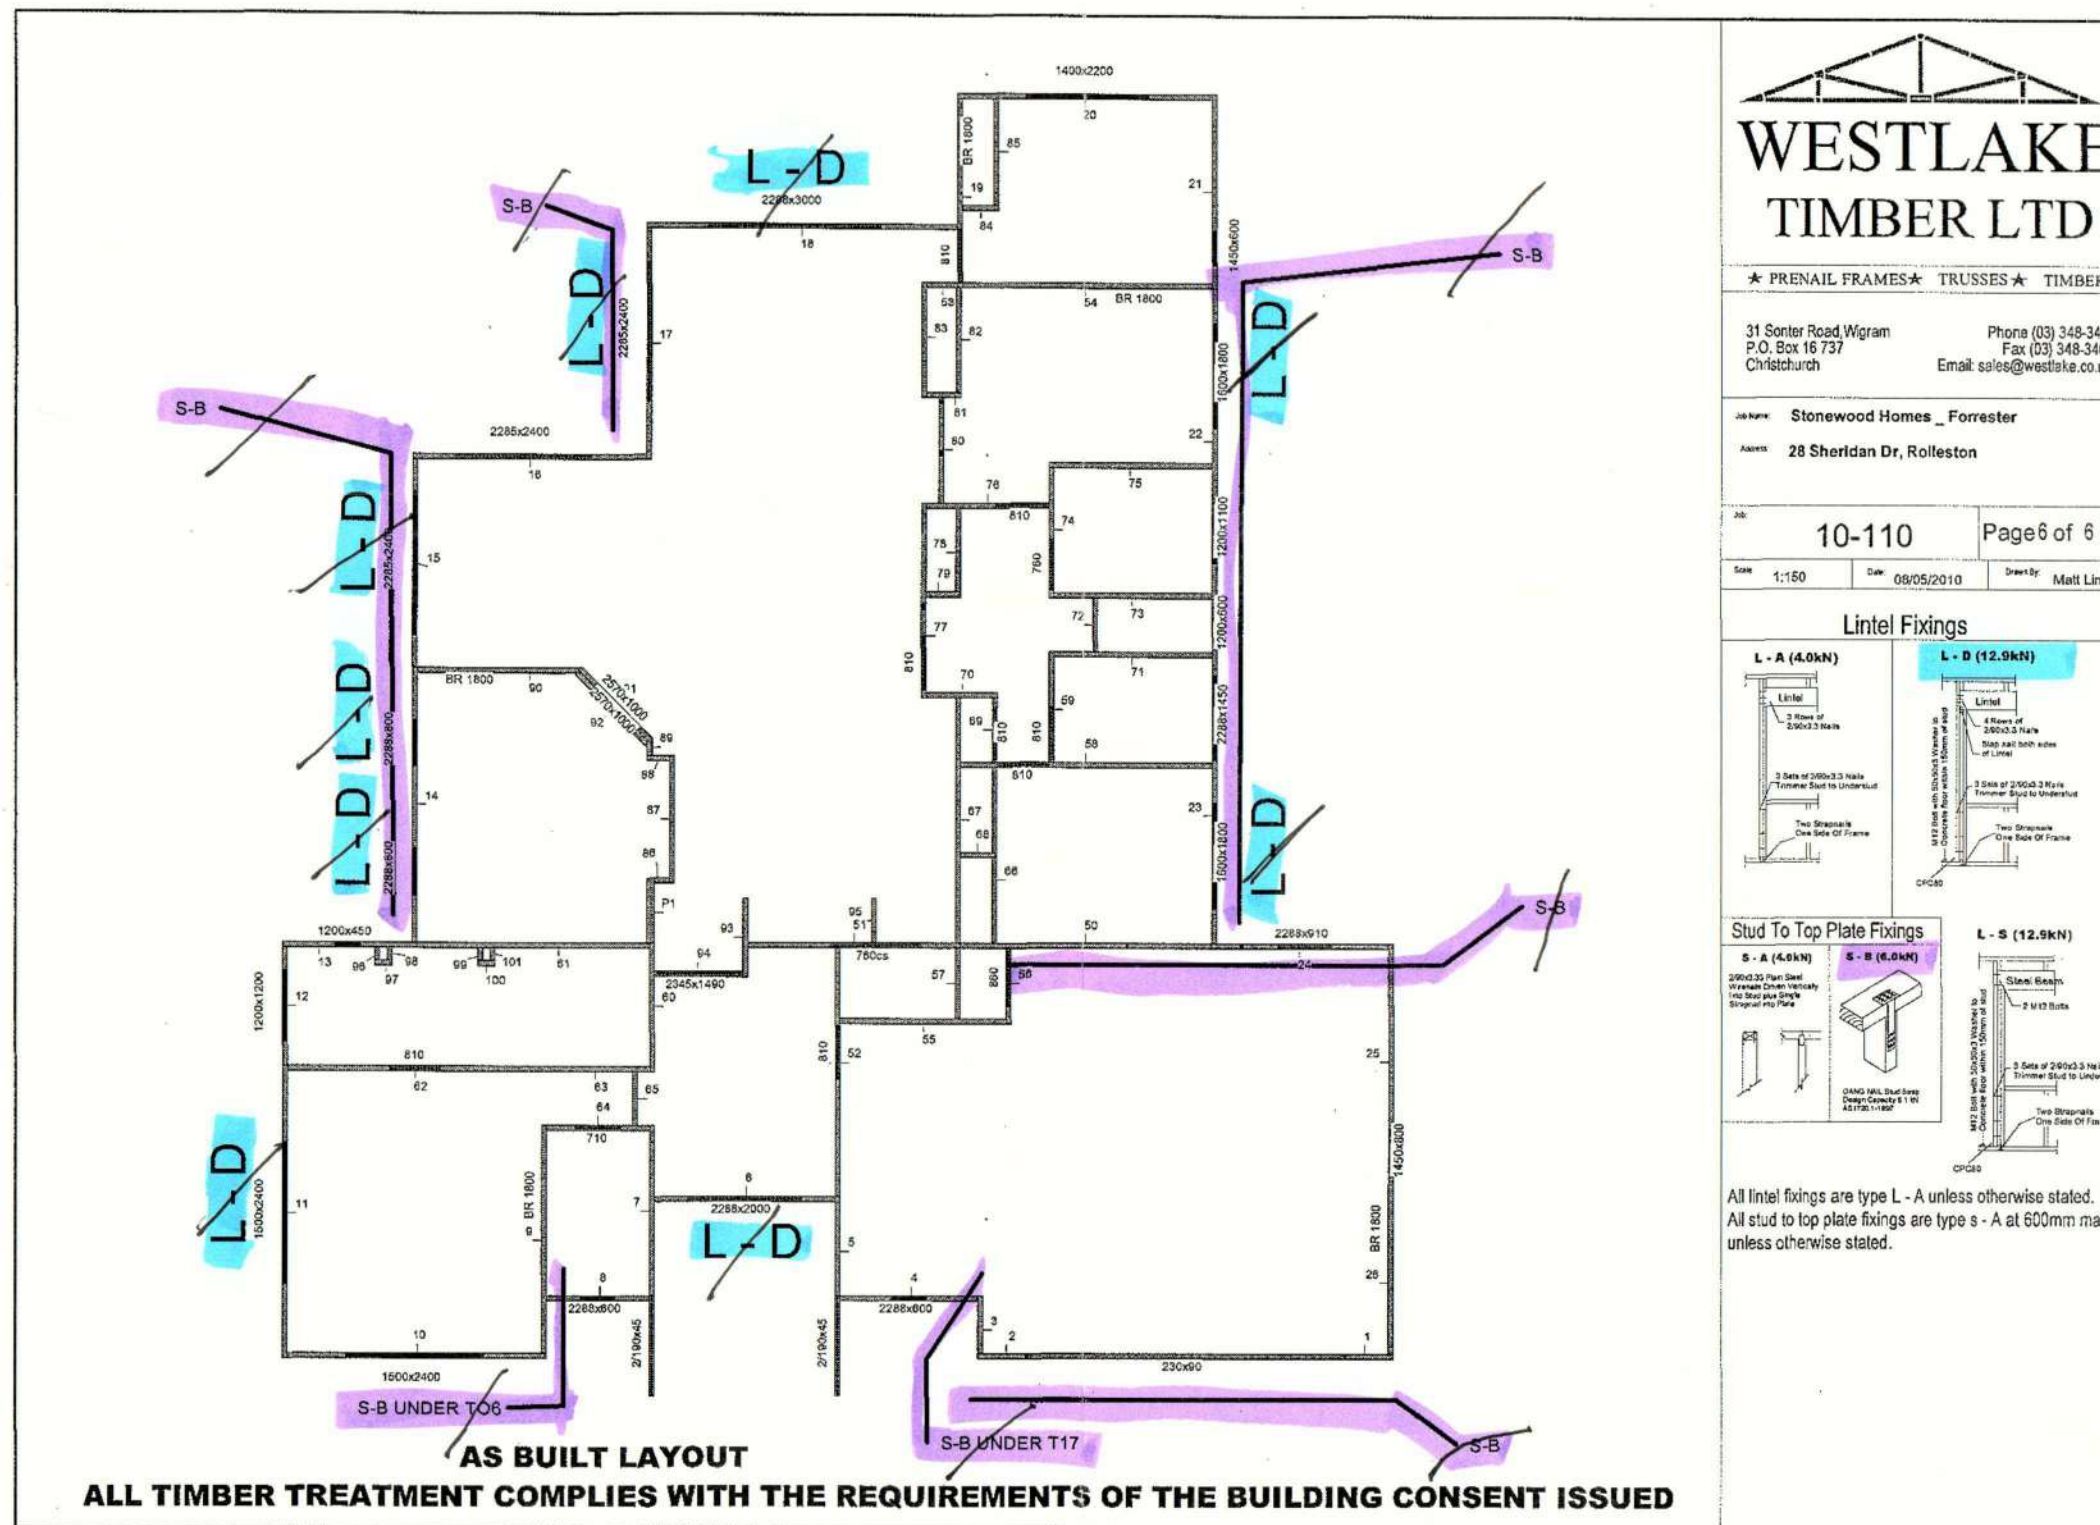

WESTLAKE TIMBER LTD

★ PRENAIL FRAMES★ TRUSSES★ TIMBER

31 Senter Road, Wigram Phone (03) 348-3401
P.O. Box 16 737 Fax (03) 348-3402
Christchurch Email sales@westlake.co.nz


Job Name: Stonewood Homes - Forrester

Address: 28 Sheridan Dr, Rolleston


Job: 10-110 Page 6 of 6
Scale: 1:150 Date: 08/05/2010 Drawn By: Matt Lintott

Lintel Fixings

L - A (4.0kN)



L - D (12.9kN)



Stud To Top Plate Fixings


S - A (4.0kN)



S - B (6.0kN)



L - S (12.9kN)



All lintel fixings are type L - A unless otherwise stated.
All stud to top plate fixings are type S - A at 600mm max unless otherwise stated.

**Inspection
File**

100223
SELWYN DISTRICT COUNCIL
13/5/10
CONSENT DOCUMENT

12 MAY 2010

INSPECTION NOTICE

Inspections are to be booked by the owner or builder.

Name: Forrester Consent No: 100223
 Site Address/Rapid No: 28 Sheridan drive Officer: 27
Rollerton Name: Chris Weir

Type of building work: Dwelling
 On 10 / 8 / 10 at 1.24 am / pm this site was inspected pursuant to the Building Act 2004 [Section 222/230] and the Local Government Act 2004 [Section 174]. The purpose of the inspection was:-

a	Siting & Founds	h	Bond Beam	o	Other
b	Slab	i	Blockfill	p	Resource Consent
c	Pre Wrap	j	Heating unit	q	Complaint/investigation
d	Post Wrap	k	Sanitary drainage	r	Compliance Schedule
e	Half height veneer	l	Stormwater drainage	s	WOF/ c/s audit
f	Preline/Plumbing	m	Pile/pole holes	t	Final Inspection
g	Post line bracing	n	Cladding	u	☐ Pass ☐ Fail

BUILDING WORK MAY PROCEED ☒ MAY NOT PROCEED ☐ RE-INSPECTION YES ☐ NO ☒

INSPECTION NOTES:

Sanitary: 100mm pvc laid on chip to a grade 1:60 to lateral

Vents + inspection points in place
 test being put on at time of inspection

Stormwater: 100 + 90mm pvc laid on chip to a grade 1:60 to soak holes.

1-1 Ensure Geo cloth is fitted

NOTE: A Code Compliance Certificate Application is required for 2004 Building Act Consents

Owner/Builder/Contractor confirms floor height is as recommended by Environment Canterbury ☐

INSTRUCTIONS

All work inspected is in accordance with the Building Consent ☐

Satisfactory: Work may proceed when minor items above have been attended to ☒

Some work is not satisfactory or is incomplete, as detailed above, and rectification is required. ☐

A notice to fix will be issued ☐

Notice to: Contractor ☒ Owner ☐ Agent ☐ Occupier ☐ Signed: Dea

By: Telephone ☐ Fax ☐ Posting ☐ Left on Site ☒

Building Consent Inspection Prompt Sheet Drainage

PROJECT DETAILS			
Building Consent No. 100223	Site Copy Viewed:	Yes ☐	No ☐
Inspector's Name: Chris W			
Time Arrived: 1.24	Time Departed:	Date: 10/5/10	

ITEMS INSPECTED	
Sewage Systems	Stormwater Systems
☒ Drain material 100	☒ Drain material 90 x 100
☒ Gradients 1:60	☒ Gradients 1:60
☒ Drain inspection points	☒ Drain inspection points
☒ Drain venting	☒ Drain venting
☒ Bedding material	☒ Bedding material chip
☒ Cover	☒ Cover
☒ Connection to lateral	☒ Connection to lateral
☒ Drain test being put on.	☒ Soakage pits
On Site Wastewater System	
☒ Septic tank	☒ Downpipe sizes
☒ Venting	☒ Downpipe positions
☒ Effluent trench depth	☒ Deck drains
☒ Trench Length	☒ Deck overflows
	☒ Gutter sizes and overflows
	☒ Bubble up sump
Advanced Systems	Other Items
☒ Dripper lines	☐ Complete the database for on site systems
☒ Disposal bed	☒ As laid plan
☒ Venting	☒ Tradesman's registration 18538
☒ Location of wastewater systems	

This is not an inspection record, it serves as a prompt and simply indicates that the items listed have been inspected. The Inspection Notice provides the record of items inspected and decisions made with respect to progression of building work, together with reasons for these decisions as inspection notes.

INSPECTION NOTICE

Inspections are to be booked by the owner or builder.

Name: Fomester Consent No: 100223

Site Address/Rapid No: Shed on Rolleston Officer: _____

Name: 1340

Type of building work: Dwelling

On 6 / 5 / 10 at _____ am / pm this site was inspected pursuant to the Building Act 2004 [Section 222/230] and the Local Government Act 2004 [Section 174]. The purpose of the inspection was:-

a	Siting & Founds	h	Bond Beam	o	Other	
b	Slab	i	Blockfill	p	Resource Consent	
c	Pre Wrap	j	Heating unit	q	Complaint/investigation	
d	Post Wrap	k	Sanitary drainage	r	Compliance Schedule	
e	Half height veneer	l	Stormwater drainage	s	WOF/ c/s audit	
f	Preline/Plumbing	m	Pile/pole holes	t	Final Inspection	☐ Pass
g	Post line bracing	n	Cladding	u		☐ Fail

BUILDING WORK MAY PROCEED ☒ MAY NOT PROCEED ☐ RE-INSPECTION YES ☐ NO ☒

INSPECTION NOTES:

Ceilings, DPM installed
 BP orders @ 900x
 665 mesh caving slab area
 5 x point load rods
 formed. Reinforcing installed.
 Services sealed to DPM & lagged.

ENTERED
TP

NOTE: A Code Compliance Certificate Application is required for 2004 Building Act Consents

Owner/Builder/Contractor confirms floor height is as recommended by Environment Canterbury ☐

INSTRUCTIONS

All work inspected is in accordance with the Building Consent ☐

Satisfactory: Work may proceed when minor items above have been attended to ☐

Some work is not satisfactory or is incomplete, as detailed above, and rectification is required. ☐

A notice to fix will be issued ☐

Notice to: Contractor ☒ Owner ☐ Agent ☐ Occupier ☐ Signed: _____

By: Telephone ☐ Fax ☐ Posting ☐ Left on Site ☐

IN REPLY TO

Dear Sir,
I have the honor to acknowledge the receipt of your letter of the 10th inst.

and in reply to inform you that the same has been forwarded to the proper authorities for their consideration.

I am, Sir, very respectfully,
Your obedient servant,

J. H. [Signature]

[Address]

[City, State]

[Date]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

[Text]

ENTERED

Building Consent Inspection Prompt Sheet Concrete Floor Slabs

PROJECT DETAILS			
Building Consent No.	100223	Site Copy Viewed:	☒ Yes ☐ No
Inspector's Name:	J Boyd		
Time Arrived:	Time Departed:	Date: 6.5.10	

ITEMS INSPECTED	
Damp Proofing	Base Course
☒ DPM	☒ Material
☒ Lapping and Sealing	☒ Depth
☒ Penetrations	☒ Compaction
☒ Edge Finishing	☒ Vegetation Removed
Reinforcing	Other Items
☒ Mesh Size	☒ Brace Fixings
☒ Lapping	☒ Framing Fixings
☒ Cover	☒ Shrinkage Control
☒ Shrinkage Rods	☒ Heating
☒ Chairs	☒ Insulation
☒ Starter Lapping	☒ Services
☒ Starter Tying	

This is not an inspection record, it serves as a prompt and simply indicates that the items listed have been inspected. The Inspection Notice provides the record of items inspected and decisions made with respect to progression of building work, together with reasons for these decisions as inspection notes.

INSPECTION NOTICE

Inspections are to be booked by the owner or builder.

Name: ItJ Forrester Consent No: 100 223
 Site Address/Rapid No: 28 Sheridan Drive Officer:
Rolleston Name: Geoff Stevenson

Type of building work: Domestic Dwelling

On 5 / 05 / 10 at 1-06 am/pm this site was inspected pursuant to the Building Act 2004 [Section 222/230] and the Local Government Act 2004 [Section 174]. The purpose of the inspection was:-

a	Siting & Foundations	h	Bond Beam	o	Other
b	Slab	i	Blockfill	p	Resource Consent
c	Pre Wrap	j	Heating unit	q	Complaint/investigation
d	Post Wrap	k	Sanitary drainage <u>under slab</u>	r	Compliance Schedule
e	Half height veneer	l	Stormwater drainage	s	WOF/ c/s audit
f	Preline/Plumbing	m	Pile/pole holes	t	Final
g	Post line bracing	n	Cladding	u	Inspection
					☐ Pass
					☐ Fail

BUILDING WORK MAY PROCEED ☐ MAY NOT PROCEED ☐ RE-INSPECTION YES ☐ NO ☐

INSPECTION NOTES:

- * 1/ w/c to ensuite will need to be backvented ~~min~~ within 15m of water seal if 1:60 Gradient is not maintained to all drains.
- * 2/ AAV is required for ensuite shower please install exceeds 3.5 m to bulky dish.
 Plans show w/c + shower to ensuite to be vented.
 All waste 40x50mm UPVC laid in max 20mm rounds.
 Gradient 1:40+. Two soil pipes installed
- * 3/ Ensuite basin + kitchen sink to be AAV at trap
 Had to wait on site for approved plans.

NOTE: A Code Compliance Certificate Application is required for 2004 Building Act Consents

Owner/Builder/Contractor confirms floor height is as recommended by Environment Canterbury ☐

INSTRUCTIONS

All work inspected is in accordance with the Building Consent ☐

Satisfactory: Work may proceed when minor items above have been attended to ☒

Some work is not satisfactory or is incomplete, as detailed above, and rectification is required. ☐

A notice to fix will be issued ☐

Notice to: Contractor ☒ Owner ☐ Agent ☐ Occupier ☐ Signed: [Signature]
 By: Telephone ☐ Fax ☐ Posting ☐ Left on Site ☐

INSPECTION NOTICE

Section 1

1. Name of the person or company to be inspected: ABC Company
 2. Address: 123 Main Street, London, EC1A 1AA
 3. Date of inspection: 15/01/2023
 4. Name of the inspector: John Smith
 5. Reason for inspection: Annual safety inspection

Item	Inspected	Defects	Remarks
1. General appearance	Yes	None	Good
2. Safety equipment	Yes	None	Good
3. Fire safety	Yes	None	Good
4. Electrical safety	Yes	None	Good
5. Gas safety	Yes	None	Good
6. Lift safety	Yes	None	Good
7. Staircase safety	Yes	None	Good
8. Other	Yes	None	Good

6. Overall condition: Good (Satisfactory / Unsatisfactory / Very Satisfactory)

7. Remarks: The premises are in good condition and all safety equipment is in good working order. No defects were observed during the inspection.

ENTERED

8. Signature of the inspector: John Smith
 9. Date of issue: 15/01/2023
 10. Validity: 12 months
 11. Notes: None

Building Consent Inspection Prompt Sheet Plumbing

PROJECT DETAILS			
Building Consent No.	100 223	Site Copy Viewed:	☒ Yes ☐ No
Inspector's Name:	Geoff Stevenson		
Time Arrived:	1-06 PM	Time Departed:	Date: 5-05-10

ITEMS INSPECTED			
Water		Wastes	
☒	Pipework	☒	Pipework
☒	Jointing	☒	Size 40+50 to showers.
☒	Support	☒	Support 20mm round Max
☒	Pressure Test	☒	Gradient 1:40+
☒	Frost Protection	☒	Air Admittance Valves ensure shower.
☒	Shut-off Valve		Discharge Level
☒	Electrical Bonding	☒	Back Venting Could be req'd for ensure w/c
☒	Cross Connection	☒	Drain Vents TO Install
		☒	Pan Vents NA
Hot Water Cylinder		Ceiling Tanks	
☒	Support	☒	Safe Tray
☒	Seismic Restraint	☒	Tray Overflow
☒	Safe Tray	☒	Air Gap
☒	Replacement	☒	Seismic Restraint
☒	Drain	☒	Support
☒	Open Vent		
☒	Frost Protection		
☒	PRV/TPR		
☒	Copper Pipe Outlet		
☒	Tundish Level		
☒	Wetback		
☒	Valving		
☒	Tempering Valve		

This is not an inspection record, it serves as a prompt and simply indicates that the items listed have been inspected. The Inspection Notice provides the record of items inspected and decisions made with respect to progression of building work, together with reasons for these decisions as inspection notes.

INSPECTION NOTICE

Inspections are to be booked by the owner or builder.

Name: Forester Consent No: 100223
 Site Address/Rapid No: Sherida Dr Rolleston Officer: [Signature]
 Name: [Signature]

Type of building work: Dwelling
 On 3 / 5 / 10 at am / pm this site was inspected pursuant to the Building Act 2004 [Section 222/230] and the Local Government Act 2004 [Section 174]. The purpose of the inspection was:-

a	☒	Siting & Founds	h		Bond Beam	o		Other
b		Slab	i		Blockfill	p		Resource Consent
c		Pre Wrap	j		Heating unit	q		Complaint/investigation
d		Post Wrap	k		Sanitary drainage	r		Compliance Schedule
e		Half height veneer	l		Stormwater drainage	s		WOF/ c/s audit
f		Preline/Plumbing	m		Pile/pole holes	t		Final
g		Post line bracing	n		Cladding	u		Inspection
								☐ Pass
								☐ Fail

BUILDING WORK MAY PROCEED ☒ MAY NOT PROCEED ☐ RE-INSPECTION YES ☐ NO ☒

INSPECTION NOTES:

Siting of dwelling confirmed by contractor as per plan.

Foundation 240mm wide into firm ground.

Reinforcing 2x D16 horizontal with D16 stakes @ top tied & supported.

Provisions for services installed.

ENTERED

NOTE: A Code Compliance Certificate Application is required for 2004 Building Act Consents

KL

Owner/Builder/Contractor confirms floor height is as recommended by Environment Canterbury ☐

INSTRUCTIONS

All work inspected is in accordance with the Building Consent ☒

Satisfactory: Work may proceed when minor items above have been attended to ☐

Some work is not satisfactory or is incomplete, as detailed above, and rectification is required. ☐

A notice to fix will be issued ☐

Notice to: Contractor ☒ Owner ☐ Agent ☐ Occupier ☐ Signed: [Signature]

By: Telephone ☐ Fax ☐ Posting ☐ Left on Site ☐

ENTERED

Building Consent Inspection Prompt Sheet Concrete Footings and Foundation Walls

PROJECT DETAILS			
Building Consent No. <u>100223</u>	Site Copy Viewed: ☐ Yes ☒ No		
Inspector's Name: <u>J. 3012</u>			
Time Arrived:	Time Departed:	Date: <u>3.5.10</u>	

ITEMS INSPECTED	
Site Factors	Steel Work
☒ Potential Flooding	☒ Horizontal Rods
☒ Distance to Boundary	☒ Vertical Rods
☒ Site Stability	☒ Starters
☒ Ground Bearing	☒ Steel Identified
☒ Vegetation Clear	☒ Bottom Cover
☒ Topsoil Removed	☒ Side Cover
☒ Overhead or close Power wires	☒ Lapping
	☒ Tying
Excavations	Other Items
☒ Depth	☒ Services Blockouts
☒ Width	Steel Around Blockouts
☒ Formwork	Finished Floor Height
☒ Level Bottom	Drains under Building
☒ Stepped Foundations	Subfloor Ventilation

This is not an inspection record; it serves as a prompt and simply indicates that the items listed have been inspected. The Inspection Notice provides the record of items inspected and decisions made with respect to progression of building work, together with reasons for these decisions as inspection notes.

This building consent is subject to the following Conditions.

Selwyn District Council Building Consent Authority Officers will carry out the following inspections:

Foundations

3-05-10 ✓

Excavation for foundations including ground bearing capacity.
Reinforcing steel in foundation before concrete is poured.
Post hole excavations.

Waste Pipes

CDS 5-05-10 ✓

Inspection and testing of sanitary plumbing before placement of granular base course underfloor slab.

Floor Slab

Todd 6-05-10 ✓

To check DPC, reinforcing/thickenings to floor slab before concrete is poured.

Pre-wrap

Chris 8-06-10 ✓

Structural framing and fixings prior to building wrap, soffit, and roofing installation.
Valley and secret gutter flashings prior to roofing installation.
Control joints and saw cuts to floor slab have been completed.

Pre-clad

*CDS 11-06-10 Fail
Peter 18-06-10 Pass ✓*

Inspection of building wrap, DPM, and flashings prior to veneer construction.

DA → Cavity battens and flashings in place, prior to cladding being fixed. *23-06-10 ✓*

Cladding Half High

Peter 18-06-10 ✓

Veneer mid height inspection for cavity width, tie fixing, and check for mortar droppings.

Building Consent 100223

Tim 30-06-10 Fail ✓
✓CMS 3-08-10 Pass ✓

Pre-line

Tim 1-07-10 Fail ✓
Daryl 16-07-10 Fail ✓

Carl 30-07-10 Fail ✓

NOTE: A weathertight exterior is required before a preline inspection occurs.

Plumbing pipe work prior to fixing of internal linings.

Preline moisture test and structural framing check including confirmation of treated timber where required.

Bracing elements prior to fixing of internal linings.

Completeness of insulation prior to fixing of internal linings.

Window installation to check ventilation, air seals, and glazing.

Plumbing & Drainage

✓CMS 10-08-10 ✓

NOTE:- All drainage work must be inspected prior to backfilling and a fully dimensioned 'as-built' drainage plan for Council records must be available when the Inspector visits the site.

Inspection and testing of sanitary sewer. ←

Connection to sewer lateral. ←

Spouting including rain water heads, overflows and downpipes.

Stormwater disposal to soakholes. ←

Post-line

CMS 6-08-10 Fail ✓
CMS 10-08-10 Pass ✓

Check nailing off of bracing panels before stopping work is carried out.

Tanking

Tim 1-09-10 ✓

Inspection of wet area, shower sealing, tanking of walls and floor substrate prior to installing surface finishes.

Practical Completion - Residential

Hot water reticulation valving.

Check temperature of hot water.

Seismic restraints to hot water cylinder and storage tanks.

Domestic mechanical ventilation.

Slip resistant surfaces.

Smoke alarm installation.

Window restrictors where appropriate.

Safety glass where appropriate.

Sealed driveway/surfaces including associated drainage.

An 'as built' truss layout, showing truss and top plate connectors, and a Producer Statement together with the lintel sizes outside the scope of NZS 3604 must be submitted to the Selwyn District Council Building Consent Authority for approval prior to the pre-wrap inspection being booked.

Upon completion of the building work Energy Work Certificates for the following items shall be provided to the owner to submit with their documentation for Code Compliance Certificate application, for the following:-

- ☐ Gasfitting
- ☐ Electrical work

Upon completion of the building work the Plumber shall provide a Pressure Test Certificate to the owner to submit with their documentation for Code Compliance Certificate application.

Advice Notes:-

When the final inspection has been carried out and all building work approved, the Code Compliance Certificate can be applied for (The Code Compliance Certificate is invoiced separately with any additional costs if applicable).

Compliance schedule

A compliance schedule is not required for this project.

Building Consent 100223

Attachments

Copies of the following documents are attached to this building consent:
Project Information Memorandum Number 100223P.

Other Approvals Required

Nil



Signature

12/04/10

Date of Granting

Selwyn District Council Building Consent Authority Signatory

Position

On behalf of: Selwyn District Council

Issue Date:

12 / APR 2010

Building Consent**100223****Section 51, Building Act 2004**

Street address of building:	28 SHERIDAN DRIVE, ROLLESTON
Legal description:	LOT 148 DP 367715
Valuation number:	2405535748
Rapid number:	
Building name:	
Building location on site:	
Level/unit number:	

Name of Owner:	I H & J I FORRESTER
----------------	---------------------

Applicant/Agent:	STONEWOOD HOMES
Contact person:	JO-ANNE AGER
Mailing address:	PO BOX 11036, SOCKBURN, CHRISTCHURCH 8443
Street address/registered office:	47 WATERLOO ROAD, CHRISTCHURCH
Phone number:	
Landline:	354 2344
Mobile:	
Daytime:	
After hours:	
Facsimile number:	354 2342
Email address:	jo-anne.ager@stonewood.co.nz
Website:	

The following building work is authorised by this building consent:

Description:	DOMESTIC DWELLING
Intended Use:	3 Bedroom Domestic Dwelling with Study & Attached Double Garage with Workshop - 300.14sqm2
Estimated Value:	\$358,421

This building consent is issued under section 51 of the Building Act 2004. This building consent does not relieve the owner of the building (or proposed building) of any duty or responsibility under any other Act relating to or affecting the building (or proposed building).

This building consent also does not permit the construction, alteration, demolition, or removal of the building (or proposed building) if that construction, alteration, demolition, or removal would be in breach of any other Act.

This Building consent is invalid unless work has commenced within 12 months from the date of issue (section 52 of Building Act 2004).

A Code Compliance Certificate must be applied for as soon as building work is completed (section 92 of Building Act 2004).

Note:- Where conflict may occur between plan/specification information and/or any other specific instruction in application documentation, the applicant and/or designer is to note that the Schedule confirming the method of compliance with the NZ Building Code **will always be the prime default control for Council.**

Any amendment to this Approved Building Consent will require approval prior to the work being carried out. This will require an Amended Building Consent application to be made.

Booking Inspections

1. The Building Consent Authority, is to be advised that the work is ready for inspection at least 1 clear working day before that inspection is required. Please note this may not guarantee an inspection at the desired time if an inspector is not available at that time.
2. All inspections are to be booked by phoning 03 347 2839 between the hours of 8:30am and 5:00pm.
3. The complete set of Approved Building Consent documents (including stamped plans and specifications) **MUST** be available on site for the Officer carrying out the inspection. No inspection will be undertaken if the approved documentation is not available.
