GASFITTING CERTIFICATE OF COMPLIANCE – GAS SAFETY CERTIFICATE

Certificate of Compliance:

Client Name: Stewart Gibson

Reference / Job #: BC130058 **ICP (if known):**

Address of work: 135 Bensmann Road

Suburb: **Town / City:** RD2 Upper Moutere

Description of gasfitting work: (If different gasfitting work was done by different people, state who did what gasfitting.)

Check and certify existing gas installation by Parlane Gas in 2013/2014. Eurotec F/S Cooker installed K6G210G and Bosch Hydropower 16. Pressure test installation pipework to 7.0kpa. No drop. Pressure test installation to 5.0kpa. No drop. Check standing pressure of regulator. Too low. Replace the auto change over regulator and check standing and running pressures. Both good.

Gas supply pressure 2.75 kPa **Risk classification** (tick one) ☐ Low-Risk ■ General ☐ High-risk

Gas type (tick one) ☐ Natural gas ■ LPG ☐ Biogas ☐ Other (specify)

The work has been done in accordance with a certified design: ☐ Yes ■ No

If yes – identify the certified design including name, date and version. Also attach a copy of the certified design to this certificate.
(Or provide reference to readily accessible electronic format, eg internet link.)

Identify:
Link:

The work relies on manufacturer's instructions: ☐ No ■ Yes

If yes – identify the instruction manual including name, date and version. Also attach a copy of manufacturer's instructions to this certificate.
(Or provide reference to readily accessible electronic format, eg internet link.)

Identify: BOSCH Hydropower Eurotec
Link: https://www.bosch-homecomfort.com/nz/media/country_pool/bosch/user_manuals/hot-water-systems/hydropower_10h_13h_16h.pdf

The work has been done in accordance with means of compliance (specify):

■ Yes – AS/NZS 5601.1 sections 3 to 6 ☐ Yes – AS/NZS 5601.2 sections 3 to 9 ☐ No

Were any other standards or gas code of practice required for compliance?

☐ Yes (specify) ■ No

Parts of the gas installation to which this certificate relates that are safe to connect to a gas supply?

■ All ☐ Parts (specify)

Date(s) on which the work was done: 27/8/2013,10+19/3/2014, 9+10/5/2023

Name and registration number of anyone who carried out work under supervision: Warren Parlane 12596

By signing this document I confirm that I am satisfied that the work described in this certificate of compliance has been done lawfully and safely, and that the information on this certificate is correct.

Certifier name: Alex Bint **Registration number:** 14856

Certifier Signature: Alex Bint Digitally signed by Alex Bint Date: 2023.05.31 08:44:05 +12'00' **Date:** 31/05/2023

Gas Safety Certificate:

By signing this document I confirm that the work described in this Gas Safety Certificate, and the installation or part installation, is connected to a gas supply and is safe to use.

Name of person authorised to certify the connection: Alex Bint

Registration number: 14856 **Date of completion or connection** 10/05/2023

Certifier Signature: Alex Bint Digitally signed by Alex Bint Date: 2023.05.31 08:44:30 +12'00' **Date:**

This Gas Safety Certificate confirms that the gasfitting work complies with the building code for the purposes of Section 19(1)(e) of the Building Act 2004.

Producer Statement - Construction

The producer statement construction does not replace the requirement for the scheduled inspection required by Tasman District Council Building Inspection Team. This producer statement construction may be an additional requirement to the scheduled inspection.

Issued to: Stewart Gibson

Issued by:
(Name) My Personal Plumber Limited

Being a suitably qualified person:
(Registration #) 14856

Address: 1366 Moutere Highway

Town: Upper Moutere

Phone: 0275424239

In respect of:
(Type of work) Gasfitting for Bosch water heater and Eurotech F/S Cooker

At: 135 Bensmann Road, Upper Moutere
Address of property

Building Consent Number: BC130058

I, Alex Bint being the

- [x] Tradesperson;
- [ ] Approved applicator; or
- [ ] Suitably qualified/experienced building practitioner.

Responsible for the work's identified above, declare that;

This work has been carried out in accordance with New Zealand Building Code Clause ..... and/or standard NZS 5601.1:2022

Signed by: Date: 31/05/2023

The above named person

Electrical Workers Registration Board

SAFETY | COMPETENCY | COMPLIANCE

Certificate of Verification

VC No: 7715

INSTALLATION DETAILS

Client: Mr & Mrs S Gibson

Address of installation (to which this certificate refers): 135 Rensemann Rd, Upper Moutere, Nelson.

Postcode 7175

THIS CERTIFICATE COVERS VERIFICATION OF:

- An existing electrical installation following disconnection from supply for greater than 6 months Reg 74 (Electrical Inspector)
- An existing installation of a caravan park in accordance with Reg 75 & AS/NZS 4801:2008 (Electrical Inspector)
- An existing installation of a boat marina in accordance with Reg 75 & AS/NZS 3004.1:2008 (Electrical Inspector)
- ✓ An existing installation on which no work has been carried out and is not subject to Regulation 73
- An MEN system of Installation
- Existing Mains work

DETAILS OF INSTALLATION VERIFICATION:

Off Grid Supply to house, Main switch board, powerpoints & Lighting circuits. Low Voltage 24V DC power supply via solar panels installed correctly, update of battery signage and DC signage recommended. RCD trip test performed

NOTE:

The COV does not satisfy the obligations under regulation 66(1)(a) if the person carries out prescribed electrical work to have the work certified. Also refer Reg 71(3)(a)(b)(c) Inspection of Prescribed Electrical Work & 74(3) Reconnection or restoring supply to certain low voltage installations.

CERTIFICATION:

I have carried out a Verification of the above installation in accordance with AS/NZS 3019:2007 and I certify the installation meets the requirements detailed in section 3, 4 or 5 of AS/NZS Standard for the issue of a Certificate of Verification.

AS/NZS 3019: 2007 in accordance with: ☐ Section 3 ✓ Section 4 ☐ Section 5

Name (name person who carried out the verification): Rowan Dorn

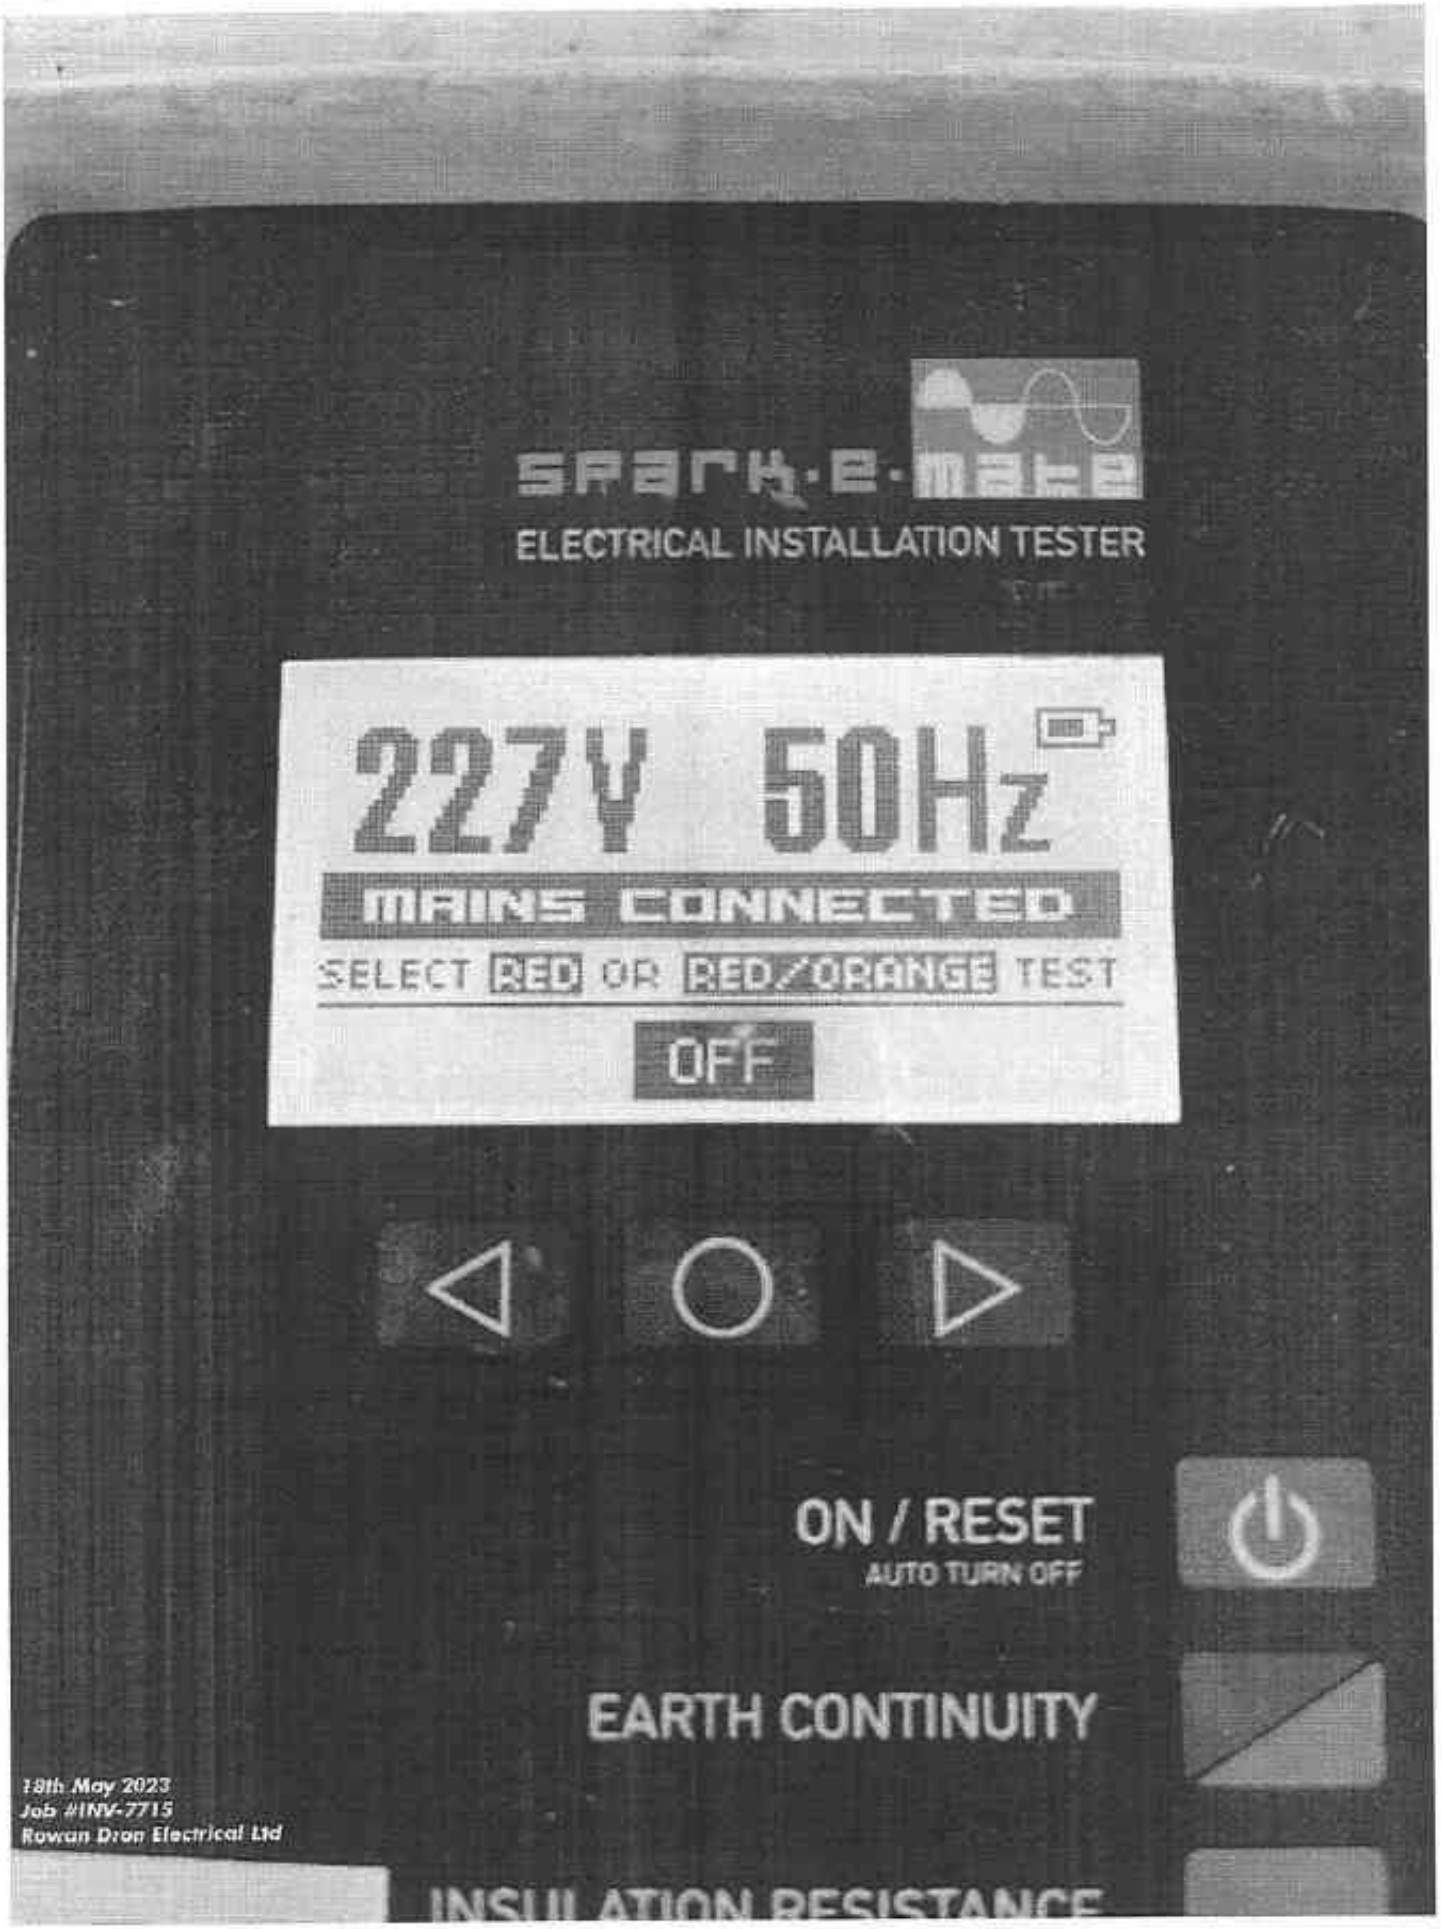
Registration Class and Number: E254383

Signature:

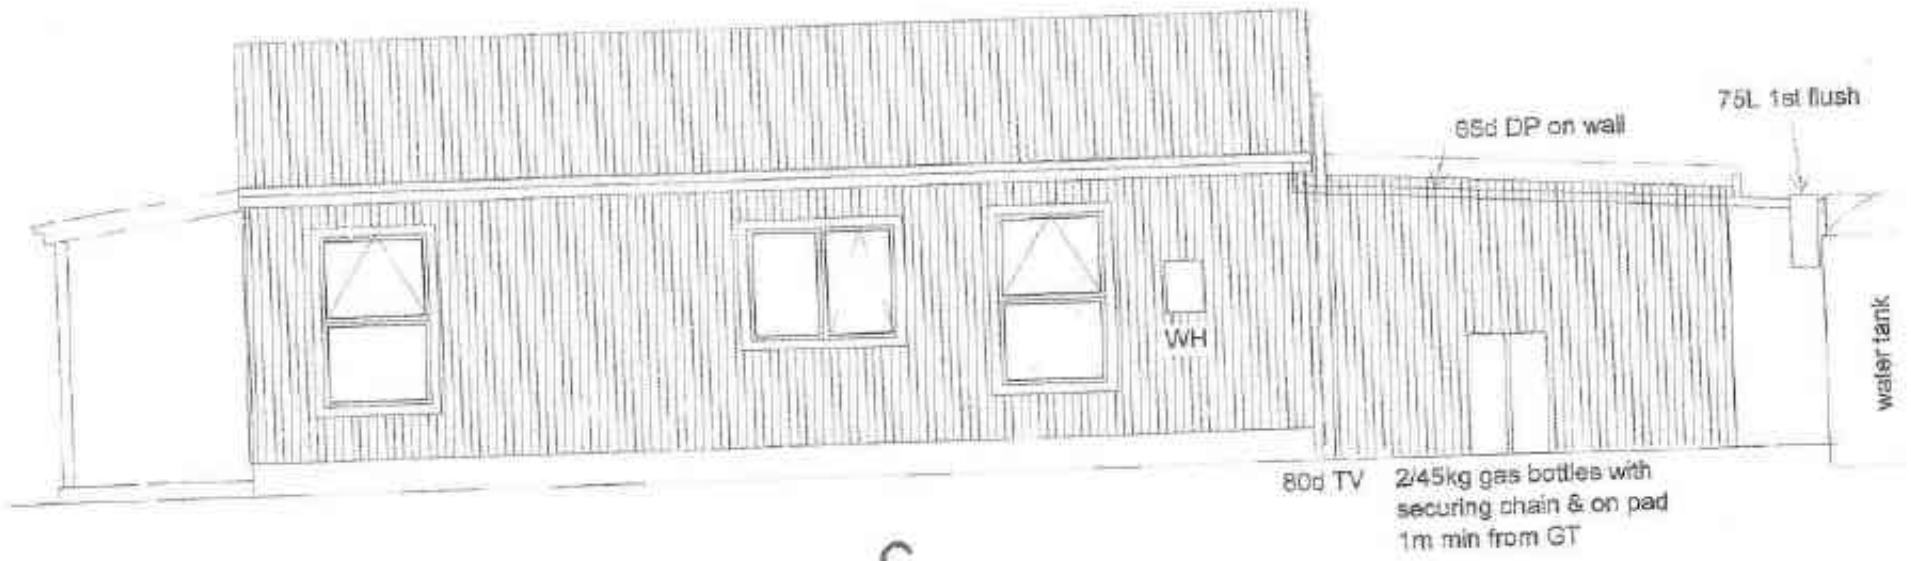
Date: 18 / 05 / 2023

ELECTRICAL INSTALLATION TESTER
POLARITY CORRECT
NO WIRING TRANSPOSITION
DETECTED-REFER TO HANDBOOK
ON / RESET
AUTO TURN OFF
EARTH CONTINUITY
INSULATION RESISTANCE
POLARITY
CIRCUIT CONNECTIONS
0800 936 574
Rowan Dron
Wakefield
Serial Number
A001091
Owner/Location
Rowan Dron
Electrical Ltd
Cal Ref #
15th May 2024
Job #INV-7215
Rowan Dron Electrical Ltd

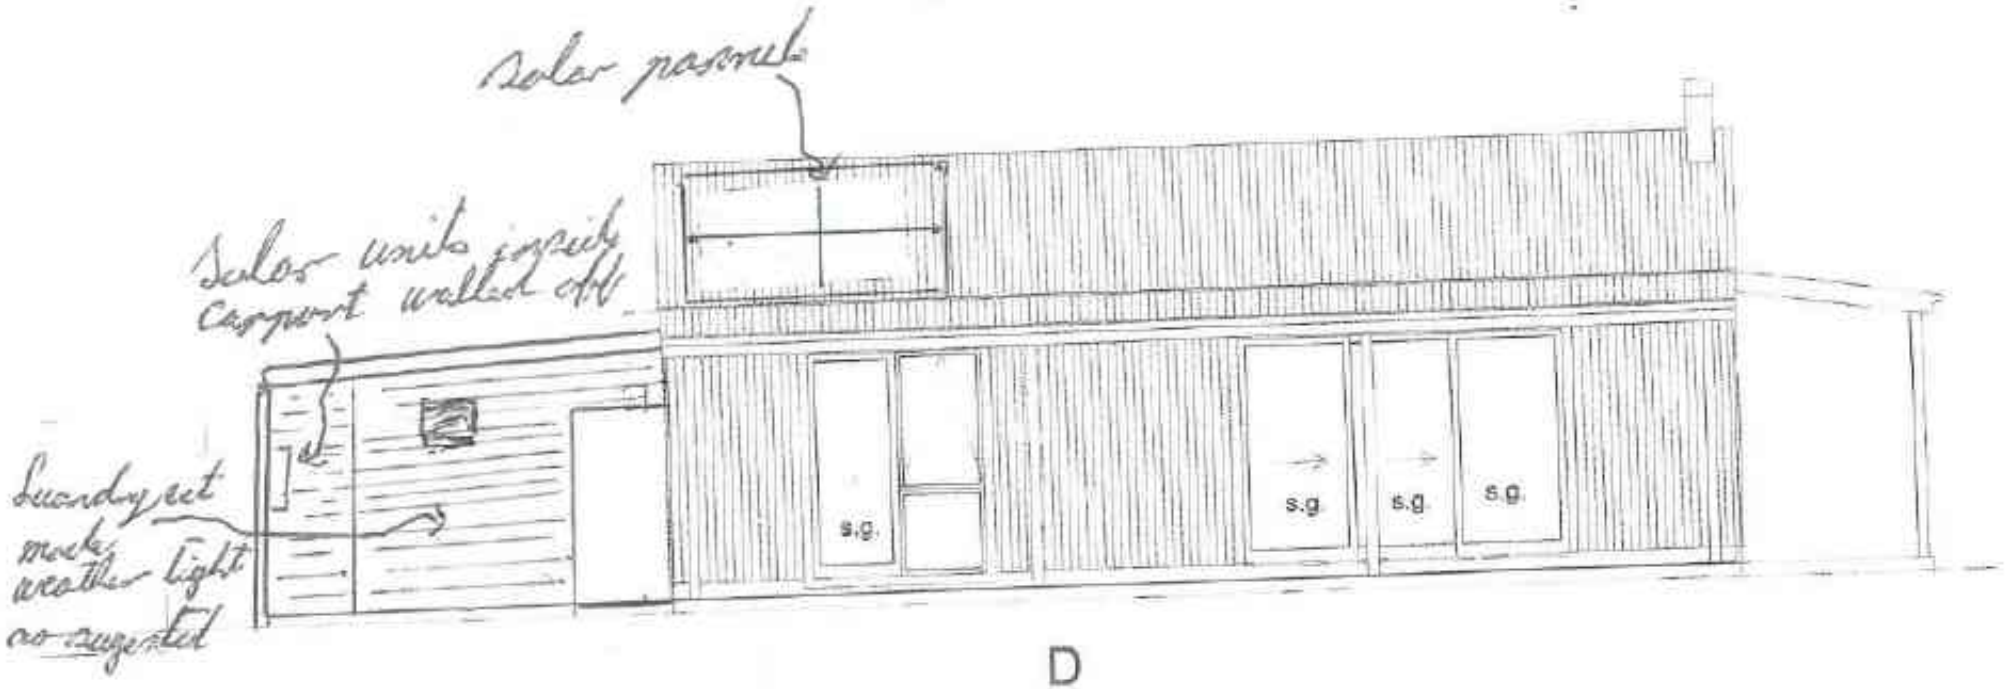
SPARK·EBT
ELECTRICAL INSTALLATION TESTER
>20 Ω (a)
Unpowered Earth Cont.
Test Complete.
INSULATION RESISTANCE
POLARITY
CIRCUIT CONNECTIONS
EARTH CONTINUITY
ON / RESET
AUTO TURN OFF
0800 935 674
Rowan Dron
Wakefield
Serial Number
A0011091
Owner/Location
Rowan Dron
Electrical Ltd
Cal Cert #
NZLD13986
18th May 2023
Job #RDE-7215
Rowan Dron Electrical Ltd


spark·e·mate
ELECTRICAL INSTALLATION TESTER
227V 50Hz
MAINS CONNECTED
SELECT RED OR RED/ORANGE TEST
OFF
ON / RESET
AUTO TURN OFF
EARTH CONTINUITY
18th May 2023
Job #INV-7715
Rowan Dron Electrical Ltd
INSULATION RESISTANCE

B


65d DP on wall
75L 1st flush
WH
water tank
80d TV
2/45kg gas bottles with
securing chain & on pad
1m min from GT

C


Solar panels
Solar units in roof
Carport walled off
Laundry ext
mesh
weather light
as suggested
s.g.
s.g.
s.g.
s.g.

D
